# Chapter 10: Project Communications Management

**Information Technology Project Management, Ninth Edition**

Note: See the text itself for full citations

Twittie Senivongse (ed.)

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Learning Objectives (1 of 2)

- Discuss the role of soft skills in IT project management, and highlight the importance of good communications as one means of achieving project success
- Review key concepts related to good communications
- Explain the elements of planning project communications and how to create a communications management plan
- Describe how to manage communications, including communication technologies, media, and performance reporting
- Discuss methods for controlling communications to ensure that information needs are met throughout the life of the project
- List various methods for improving project communications, such as running effective meetings, using various technologies effectively, and using templates

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Learning Objectives (2 of 2)

- Describe how software can enhance project communications management
- Discuss considerations for agile/adaptive environments

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# The Importance of Project Communications Management

- Greatest threat to many projects is a failure to communicate
  - You cannot totally separate technical skills and soft skills when working on IT projects
  - For projects to succeed, every project team member needs both types of skills
- Project managers say they spend as much as 90 percent of their time communicating

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Keys to Good Communications (1 of 2)

- Good communications consider size of the group, type of information, and appropriate communication medium
- Several important concepts can help
  - Focus on group and individual communication needs
    - Every person is unique, so you cannot simply generalize based on a personality profile or other traits
  - Use formal and informal methods for communicating
    - Many people prefer informal communications
    - Oral communication also helps build stronger relationships among project personnel and project stakeholders
  - Distribute important information in an effective and timely manner
    - Document any changes in technical specifications that might affect product performance
    - Report bad news
    - Have short, frequent meetings
  - Setting the stage for communicating bad news
    - Evaluate the impact of the situation
    - Consider alternatives
    - Make a recommendation to mitigate a problem

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Keys to Good Communications (2 of 2)

- Several important concepts can help (cont.)
  - Determining the number of communication channels
    - Number of communications channels = $n(n\text{-}1)/2$, where $n$ is the number of people involved
      - Limit the size of teams to avoid making communications too complex




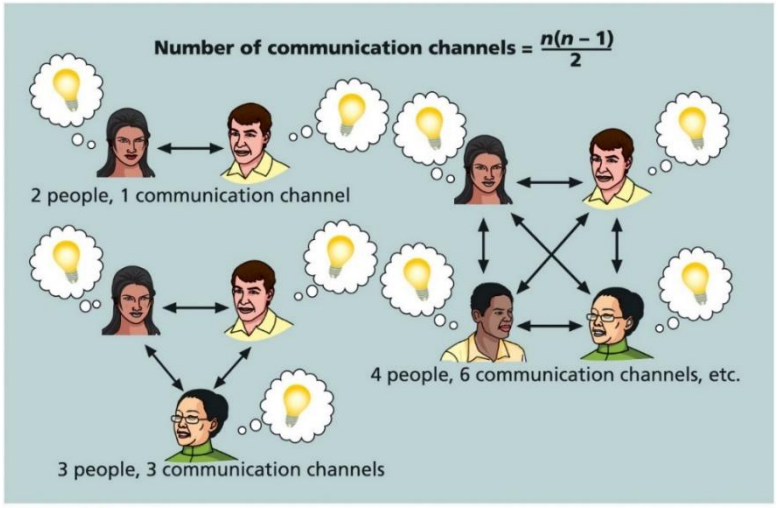



FIGURE 10-2 The impact of the number of people on communication channels

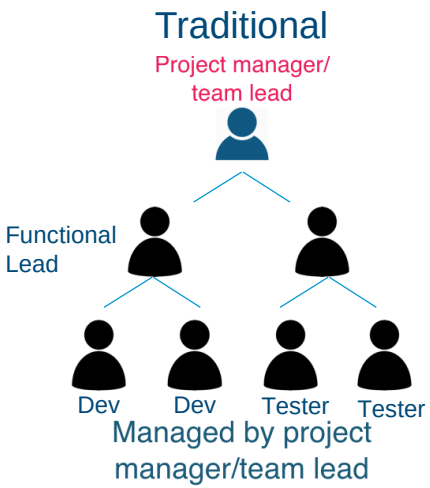

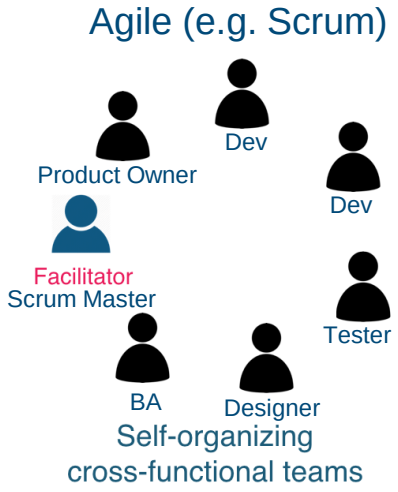


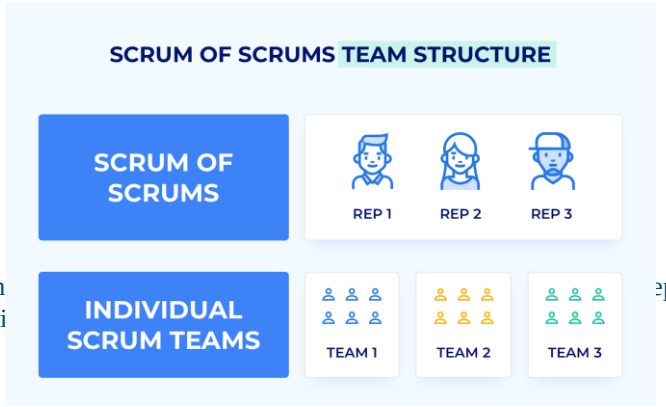

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May n ept for use as permitted in a license distributed with a certain product or service or otherwi

# Project Communications Management

- Main processes
  1. Planning communications management
     - Determining who needs what information, when they will need it, and how the information will be given to them
  2. Managing communications
     - Creating, distributing, storing, retrieving, and disposing of project communications based on the communications management plan
  3. Monitoring communications
     - Ensuring that stakeholder communication needs are met

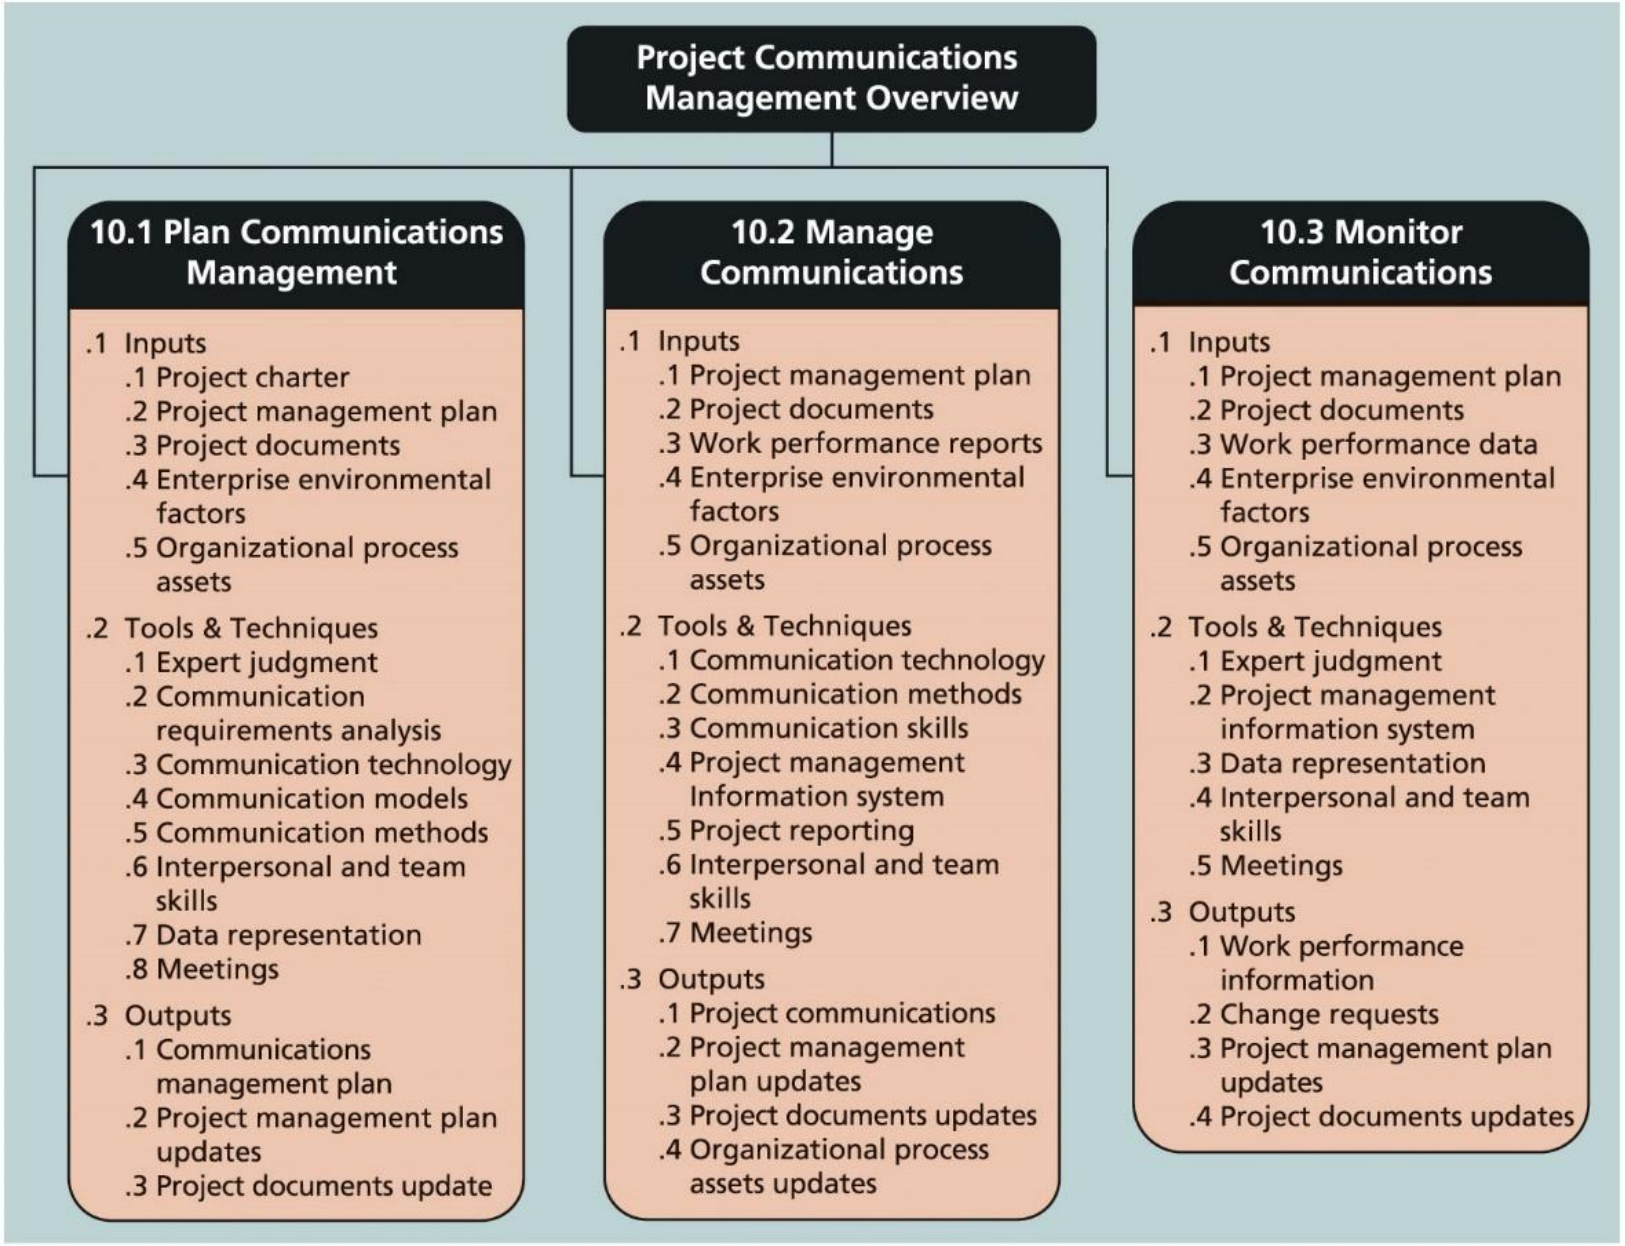Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.




Source: *PMBOK® Guide – Sixth Edition*. Project Management Institute, Inc. (2017). Copyright and all rights reserved. Material from this publication has been reproduced with permission of PMI.



**FIGURE 10-1** Project communications management overview

# 1. Planning Communications Management (1 of 2)

- For small projects, the communications management plan can be part of the team contract/charter
- For large projects, it should be a separate document
- Communications management plan contents
  - Stakeholder communications requirements
  - Information to be communicated, including format, content, and level of detail
  - Who will receive the information and who will produce it
  - Suggested methods or technologies for conveying the information
  - Frequency of communication
  - Escalation procedures for resolving issues
  - Revision procedures for updating the communications management plan
  - A glossary of common terminology

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Planning Communications Management (2 of 2)

| Stakeholders | Document Name | Document Format | Contact Person | Due |
|---|---|---|---|---|
| Customer management | Monthly status report | Hard copy and meeting | Tina Erndt, Tom Silva | First of month |
| Customer business staff | Monthly status report | Hard copy | Julie Grant, Sergey Cristobal | First of month |
| Customer technical staff | Monthly status report | E-mail | Li Chau, Nancy Michaels | First of month |
| Internal management | Monthly status report | Hard copy and meeting | Bob Thomson | First of month |
| Internal business and technical staff | Monthly status report | Intranet | Angie Liu | First of month |
| Training subcontractor | Training plan | Hard copy | Jonathan Kraus | November 1 |
| Software subcontractor | Software implementation plan | E-mail | Najwa Gates | June 1 |

Comments: Put the titles and dates of documents in e-mail headings and have recipients acknowledge receipt.

Table 10-1 Sample stakeholder communications analysis

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# 2. Managing Communications

- Managing communications is a large part of a project manager's job
  - Getting project information to the right people at the right time and in a useful format is just as important as developing the information in the first place
- Important considerations
  - Using technology to enhance information creation and distribution
  - Selecting appropriate communication methods and media
  - Reporting Performance

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Using Technology to Enhance Creation and Distribution

- Technology can facilitate the process of creating and distributing information, when used effectively, e.g.
  - Email, instant messaging, websites, phones, texting
  - Project management information systems, collaboration tools
  - Audio, video, conference call, video conferencing

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Selecting the Appropriate Communication Methods and Media

- Classifications for communication methods
  - Interactive communication
    - Two or more people interact to exchange information via meetings, phone calls, or video conferencing
      - Most effective way to ensure common understanding
  - Push communication
    - Information is sent or pushed to recipients without their request via reports, e-mails, faxes, voice mails, and other means
      - Ensures that the information is distributed, but does not ensure that it was received or understood
  - Pull communication
    - Information is sent to recipients at their request via websites, bulletin boards, e-learning, knowledge repositories like blogs, and other means

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

**TABLE 10-3** Media choice table

| KEY: 1 = EXCELLENT 2 = ADEQUATE 3 = INAPPROPRIATE | | | | | | |
|---|---|---|---|---|---|---|
| How Well Medium Is Suited to: | Hard Copy | Phone Call | Voice Mail | E-mail | Meeting | Web Site |
| Assessing commitment | 3 | 2 | 3 | 3 | 1 | 3 |
| Building consensus | 3 | 2 | 3 | 3 | 1 | 3 |
| Mediating a conflict | 3 | 2 | 3 | 3 | 1 | 3 |
| Resolving a misunderstanding | 3 | 1 | 3 | 3 | 2 | 3 |
| Addressing negative behavior | 3 | 2 | 3 | 2 | 1 | 3 |
| Expressing support/appreciation | 1 | 2 | 2 | 1 | 2 | 3 |
| Encouraging creative thinking | 2 | 3 | 3 | 1 | 3 | 3 |
| Making an ironic statement | 3 | 2 | 2 | 3 | 1 | 3 |
| Conveying a reference document | 1 | 3 | 3 | 3 | 3 | 2 |
| Reinforcing one's authority | 1 | 2 | 3 | 3 | 1 | 1 |
| Providing a permanent record | 1 | 3 | 3 | 1 | 3 | 3 |
| Maintaining confidentiality | 2 | 1 | 2 | 3 | 1 | 3 |
| Conveying simple information | 3 | 1 | 1 | 1 | 2 | 3 |
| Asking an informational question | 3 | 1 | 1 | 1 | 3 | 3 |
| Making a simple request | 3 | 1 | 1 | 1 | 3 | 3 |
| Giving complex instructions | 3 | 3 | 2 | 2 | 1 | 2 |
| Addressing many people | 2 | 3 or 1* | 2 | 2 | 3 | 1 |

*Depends on system functionality

See Tess Galati, *Email Composition and Communication (EmC2)*. Practical Communications, Inc. (*www.praccom.com*) (2001).

Information Techn
for use as permitte
or in part, except
oom use.

# Reporting Performance

- Performance reporting keeps stakeholders informed about how resources are being used to achieve project objectives
  - Progress reports describe what the project team has accomplished during a certain period of time
  - Status reports describe where the project stands at a specific point in time
  - Forecasts predict future project status and progress based on past information and trends, e.g. estimate at completion, estimated time to complete, to-complete performance index

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# 3. Monitoring Communications

- Main goal of monitoring communications is to ensure the optimal flow of information throughout the entire project life cycle
  - The project manager and project team should use expert judgment, project management information systems, data representation, interpersonal and team skills, and meetings to assess how well communications are working
  - If problems exist, the project manager and team need to take action, which often requires changes to the earlier processes of planning and managing project communications

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Suggestions for Improving Project Communications (1 of 2)

- Develop better communication skills
  - Most IT professionals enter the field because of technical skills, while communication skills training is needed
- Run effective meetings
  - Determine if the meeting can be avoided
  - Define the purpose and intended outcome of the meeting
  - Determine who should attend the meeting
  - Provide an agenda to participants before the meeting
  - Prepare handouts and visual aids and make logistical arrangements ahead of time
  - Run the meeting professionally
  - Set the ground rules for the meeting

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Suggestions for Improving Project Communications (2 of 2)

- Use e-mail and other technologies effectively
  - Be sure to send information to the right people
  - Use meaningful subject lines and limit the content of emails to one main subject
  - Be as clear and concise as possible
  - Reread your e-mail before you send it
  - Limit the number and size of e-mail attachments
  - Delete e-mail that you do not need to save or that does not require a response, e.g. junk mail
  - Make sure the virus protection software is up to date
  - Respond to e-mail quickly
  - If you need to keep e-mail, file each message appropriately
- Employ templates for project communications
  - Providing examples and templates for project communications saves time and money
  - Finding, developing, and sharing relevant templates and sample documents are important tasks for many project managers

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.


# Using Software to Assist in Project Communications (1 of 5)

- Many organizations are discovering how valuable project management software can be in communicating project information across the organization
  - Project management software can provide different views of information to help meet various communication needs
  - Many project management software products also provide tools to enhance communications
    - Portfolio management
    - Resource management
    - Project collaboration
- Even with all of the technology available, many organizations have problems communicating on global projects
  - Issues with timing, audio, and video
  - Differences in culture and language

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Using Software to Assist in Project Communications (2 of 5)

Project Management Software

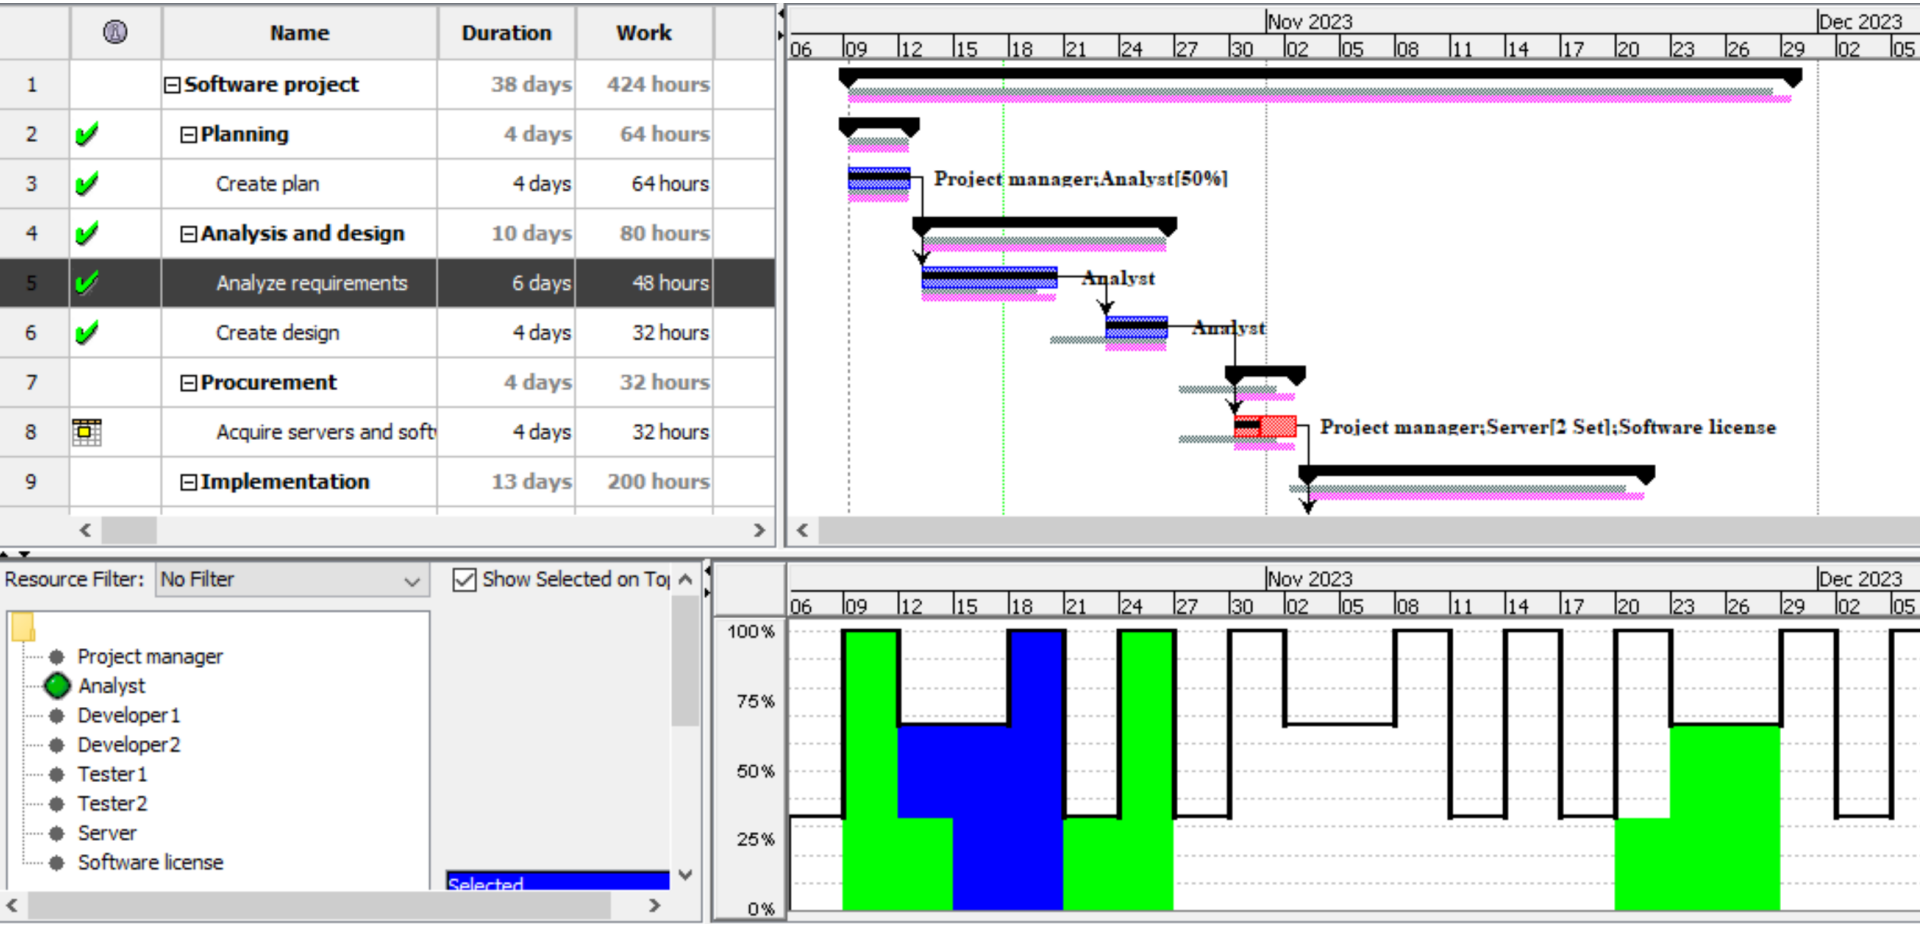



Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.


# Using Software to Assist in Project Communications (3 of 5)

Jira Agile Reporting

Scrum Board

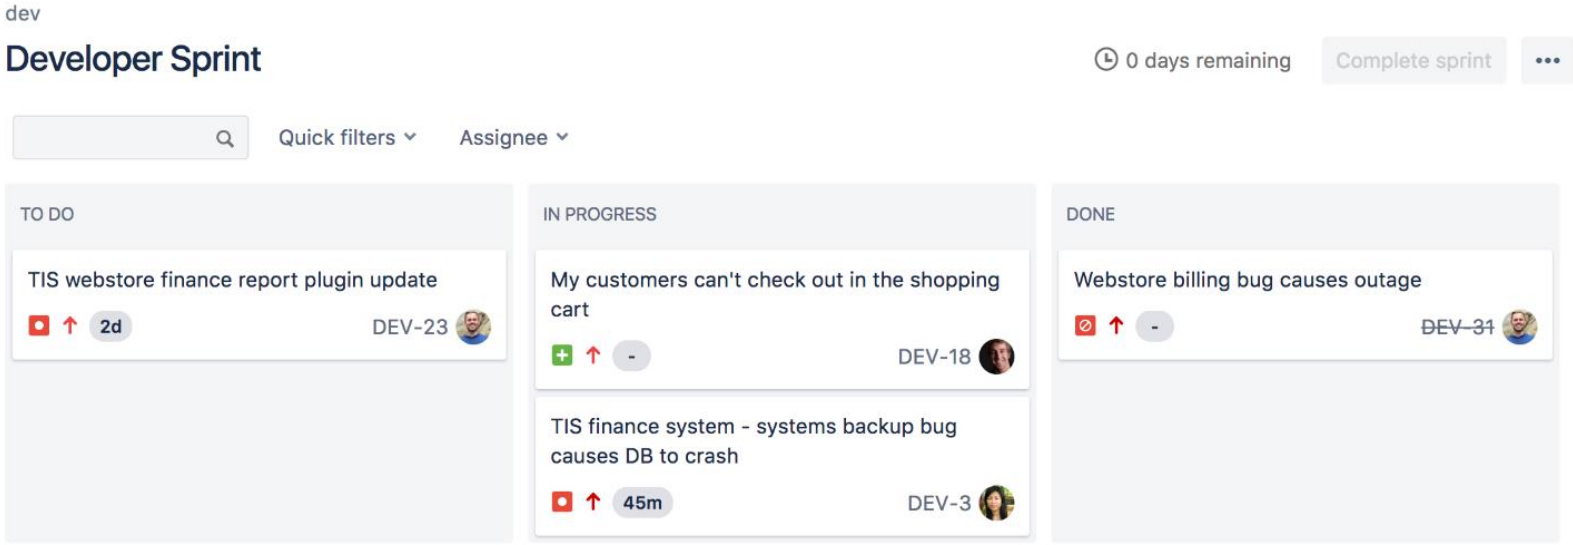



Burndown Chart

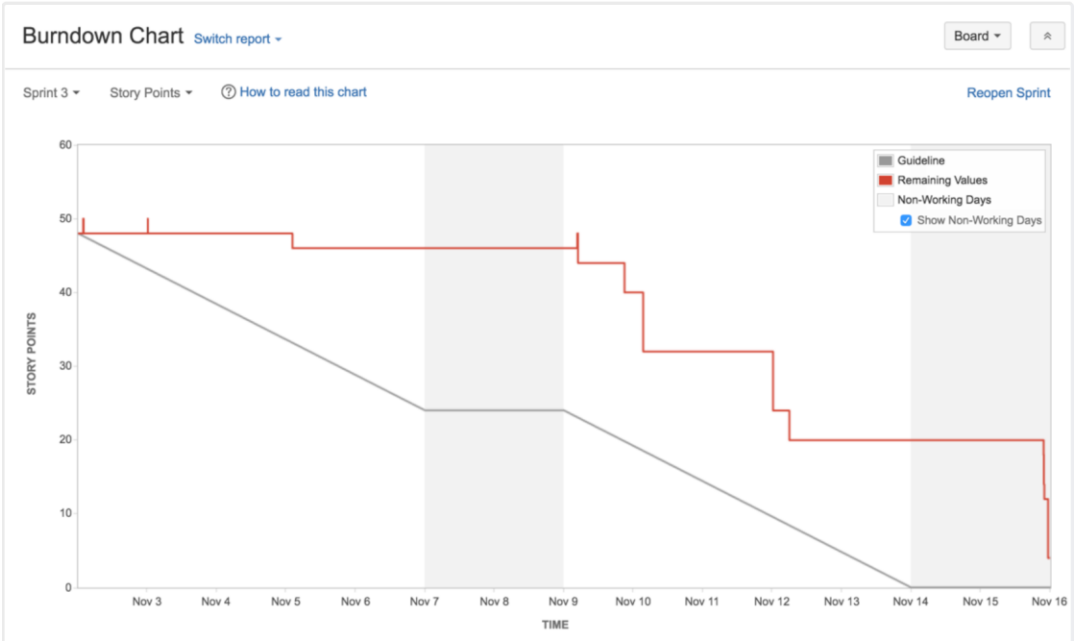

# Using Software to Assist in Project Communications (4 of 5)



# Using Software to Assist in Project Communications (5 of 5)

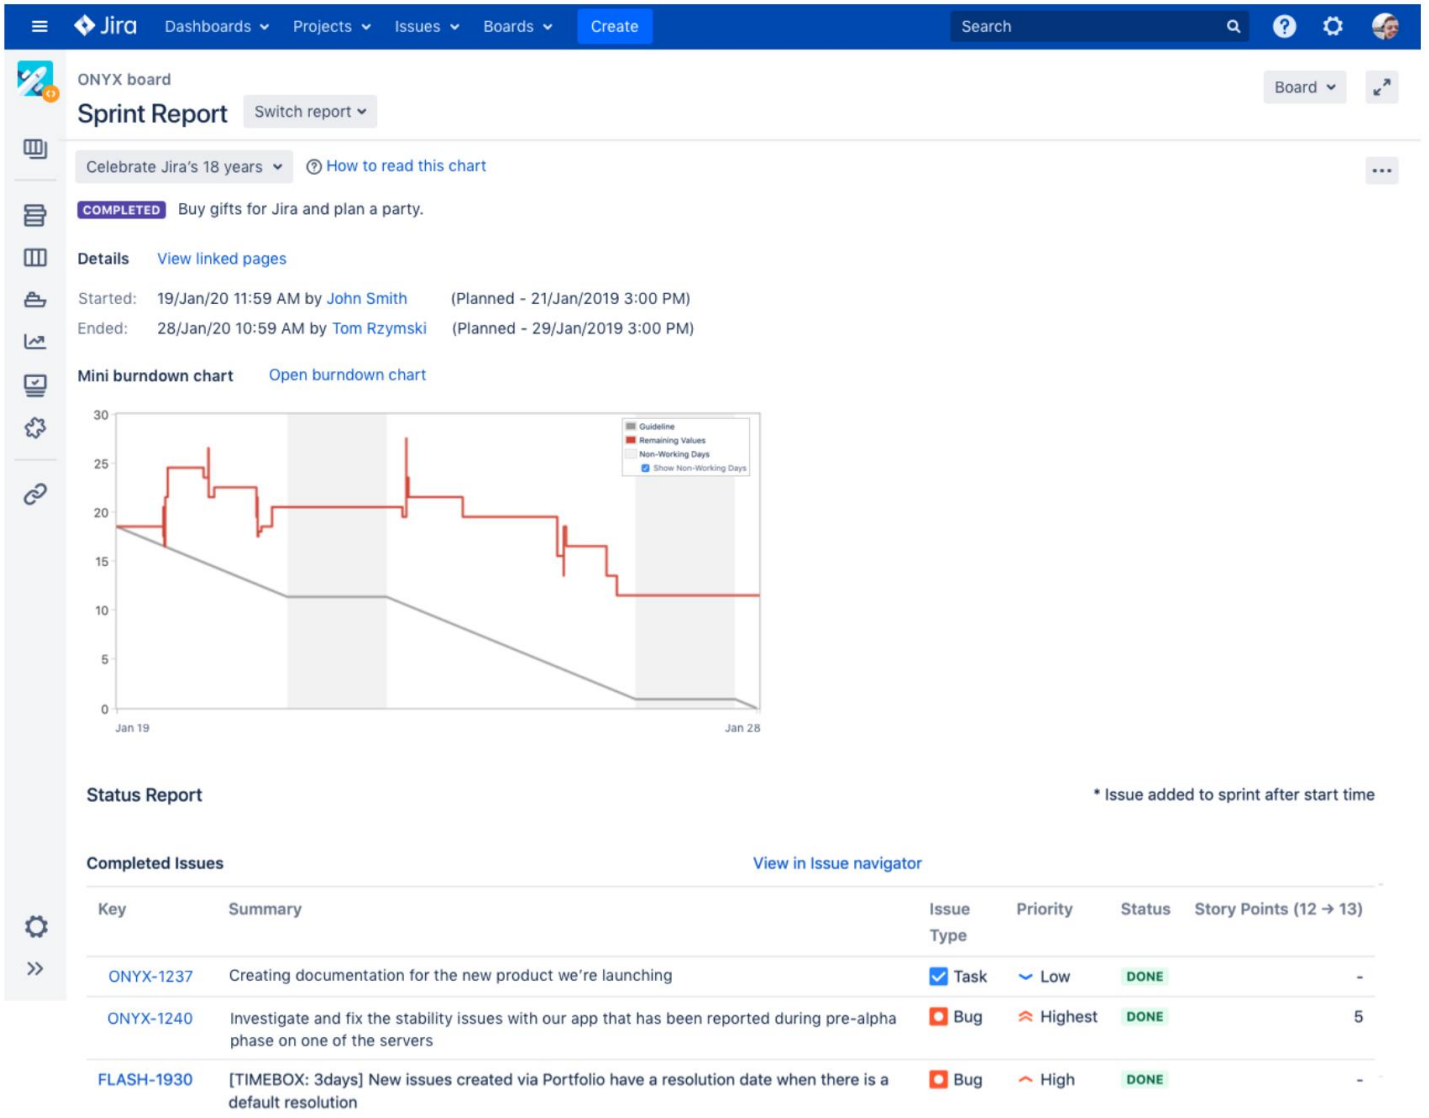


*Screenshot: Sprint Report*

# Considerations For Agile/Adaptive Environments

- Communicating evolving and emerging details frequently
- Streamlining team members to access to information, frequent team checkpoints, and collocating team members
- Holding regular stakeholder reviews promotes communication with management and stakeholders

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Chapter Summary (1 of 2)

- Failure to communicate is often the greatest threat to the success of any project, especially IT projects
  - Communication is the oil that keeps a project running smoothly
  - Project communications management involves planning communications management, managing communications, and controlling communications
- Project managers can spend as much as 90 percent of their time on communicating
  - There are several keys to good communications
- A communications management plan of some type should be created for all projects to help ensure good communications
  - Contents will vary based on the needs of the project

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

# Chapter Summary (2 of 2)

- Managing communication includes creating and distributing project information
  - Various methods for distributing project information include formal, informal, written, and verbal
- To improve project communications, project managers and their teams must develop their communication skills
  - Suggestions for improving project communications include learning how to run more effective meetings, how to use e-mail, instant messaging, texting, kanban boards, and collaborative software more effectively, and how to use templates for project communications
- New hardware and software continue to become available to help improve communications.

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.
