JWD's attachment documents

Pre-initiation

1. Business case

TABLE 3-2 JWD Consulting's business case

1.0 Introduction/Background

JWD Consulting's core business goal is to provide world-class project management consulting services to various organizations. The firm can streamline operations and increase business by providing information related to project management on its intranet site, making some information and services accessible to current and potential clients.

2.0 Business Objective

JWD Consulting's strategic goals include continuing growth and profitability. The project management intranet site project will support these goals by increasing visibility of the firm's expertise to current and potential clients by allowing client and public access to some sections of the intranet. The project will also improve profitability by reducing internal costs by providing standard tools, techniques, templates, and project management knowledge to all internal consultants.

(*continued*)

TABLE 3-2 JWD Consulting's business case (*continued*)

3.0 Current Situation and Problem/Opportunity Statement

JWD Consulting has a corporate website as well as an intranet. The firm currently uses the website for marketing information. The primary use of the intranet is for consultant human resource information, such as entering hours on projects, changing and viewing benefits information, and accessing an online directory and Web-based e-mail system. The firm also uses an enterprise-wide project management system to track all project information, focusing on the status of deliverables and meeting scope, time, and cost goals. There is an opportunity to provide a new section on the intranet dedicated to sharing consultants' project management knowledge across the organization. JWD Consulting only hires experienced consultants and gives them freedom to manage projects as they see fit. However, as the business grows and projects become more complex, even experienced project managers are looking for suggestions on how to work more effectively.

4.0 Critical Assumptions and Constraints

The proposed intranet site must be a valuable asset for JWD Consulting. Current consultants and clients must actively support the project, and it must pay for itself within one year by reducing internal operating costs and generating new business. The Project Management Office manager must lead the effort, and the project team must include participants from several parts of the company, as well as from current client organizations. The new system must run on existing hardware and software, and it should require minimal technical support. It must be easily accessible by consultants and clients and be secure from unauthorized users.

5.0 Analysis of Options and Recommendation

There are three options for addressing this opportunity:

1. Do nothing. The business is doing well, and we can continue to operate without this new project.
2. Purchase access to specialized software to support this new capability with little in-house development.
3. Design and implement the new intranet capabilities in-house, using mostly existing hardware and software.

Based on discussions with stakeholders, we believe that option 3 is the best option.

6.0 Preliminary Project Requirements

The main features of the project management intranet site include the following:

1. Access to several project management templates and tools. Users must be able to search for templates and tools, read instructions for using these templates and tools, and see examples of how to apply them to real projects. Users must also be able to submit new templates and tools, which should first be screened or edited by the Project Management Office.

(continued)

TABLE 3-2 JWD Consulting's business case (*continued*)

2. Access to relevant project management articles. Many consultants sense an information overload when they research project management information. They often waste time they should be spending with their clients. The new intranet should include access to important articles on project management topics, which are searchable by topic, and should allow users to ask the Project Management Office staff to find additional articles to meet their needs.
3. Links to other, up-to-date websites, with brief descriptions of the main features of the external sites.
4. An Ask the Expert feature to help build relationships with current and future clients and share knowledge with internal consultants.
5. Appropriate security to make the entire intranet site accessible to internal consultants and certain sections accessible to others.
6. The ability to charge money for access to some information. Some of the information and features of the intranet site should prompt external users to pay for the information or service. Payment options should include credit card or similar online payment transactions. After the system verifies payment, the user should be able to access or download the desired information.
7. Other features suggested by users, if they add value to the business.

7.0 Budget Estimate and Financial Analysis

A preliminary estimate of costs for the entire project is $140,000. This estimate is based on the project manager working about 20 hours per week for six months and other internal staff working a total of about 60 hours per week for six months. The customer representatives would not be paid for their assistance. A staff project manager would earn $50 per hour. The hourly rate for the other project team members would be $70 per hour, because some hours normally billed to clients may be needed for this project. The initial cost estimate also includes $10,000 for purchasing software and services from suppliers. After the project is completed, maintenance costs of $40,000 are included for each year, primarily to update the information and coordinate the Ask the Expert feature and online articles.

Projected benefits are based on a reduction in hours that consultants spend researching project management information, appropriate tools, and templates. Projected benefits are also based on a small increase in profits due to new business generated by this project. If each of 400 consultants saved just 40 hours each year (less than one hour per week) and could bill that time to projects that generate a conservative estimate of $10 per hour in profits, then the projected benefit would be $160,000 per year. If the new intranet increased business by just 1 percent, using past profit information, increased profits due to new business would be at least $40,000 each year. Total projected benefits, therefore, are about $200,000 per year. Exhibit A summarizes the projected costs and benefits and shows the estimated net present value (NPV), return on investment (ROI), and year in which payback occurs. It also lists assumptions made in performing this preliminary financial analysis. All of the financial estimates are very encouraging. The estimated payback is within one year, as requested by the sponsor. The NPV is $272,800, and the discounted ROI based on a three-year system life is excellent at 112 percent.

(*continued*)

TABLE 3-2 JWD Consulting's business case (*continued*)

8.0 Schedule Estimate

The sponsor would like to see the project completed within six months, but there is some flexibility in the schedule. We also assume that the new system will have a useful life of at least three years.

9.0 Potential Risks

This project carries several risks. The foremost risk is a lack of interest in the new system by our internal consultants and external clients. User inputs are crucial for populating information into this system and realizing the potential benefits from using the system. There are some technical risks in choosing the type of software used to search the system, implement security, process payments, and so on, but the features of this system all use proven technologies. The main business risk is investing the time and money into this project and not realizing the projected benefits.

10.0 Exhibits

Exhibit A: Financial Analysis for Project Management Intranet Site Project

Discount rate	8%				
Assume the project is done in about 6 months		Year			
	0	1	2	3	Total
Costs	140,000	40,000	40,000	40,000	
Discount factor	1	0.93	0.86	0.79	
present value → Discounted costs	140,000	37,037	34,294	31,753	243,084
Benefits	0	200,000	200,000	200,000	
Discount factor	1	0.93	0.86	0.79	
Discounted benefits	0	186,185	171,468	158,766	515,419
Discounted benefits - costs	(140,000)	148,148	137,174	127,013	
Cumulative benefits - costs	(140,000)	8,148	145,322	272,336 ← NPV	
	Payback in Year 1				
Discounted life cycle ROI---------->	112%				

Assumptions	
Costs	# hours
PM (500 hours, $50/hour)	25,000
Staff (1,500 hours, $70/hour)	105,000
Outsourced software and services	10,000
Total project costs (all applied in year 0)	140,000
Benefits	
# consultants	400
Hours saved	40
$/hour profit	10
Benefits from saving time	160,000
Benefits from 1% increase in profits	40,000
Total annual projected benefits	200,000

Project Initiation

1. Project charter

TABLE 3-6 Project charter

Project Title: Project Management Intranet Site Project
Project Start Date: May 2 **Projected Finish Date:** November 4

Budget Information: The firm has allocated $140,000 for this project. The majority of costs for this project will be internal labor. An initial estimate provides a total of 80 hours per week.

Project Manager: Erica Bell, (310) 555-5896, erica_bell@jwdconsulting.com

Project Objectives: Develop a new capability accessible on JWD Consulting's intranet site to help internal consultants and external customers manage projects more effectively. The intranet site will include several templates and tools that users can download, examples of completed templates and related project management documents used on real projects, important articles related to recent project management topics, an article retrieval service, links to other sites with useful information, and an Ask the Expert feature, where users can post questions about their projects and receive advice from experts in the field. Some parts of the intranet site will be accessible free to the public, other parts will only be accessible to current customers and internal consultants, and other parts will be accessible for a fee.

Main Project Success Criterion: The project should pay for itself within one year of completion.

(*continued*)

TABLE 3-6 Project charter (*continued*)

Approach:

- Develop a survey to determine critical features of the new intranet site and solicit input from consultants and customers.
- Review internal and external templates and examples of project management documents.
- Research software to provide security, manage user inputs, and facilitate the article retrieval and Ask the Expert features.
- Develop the intranet site using an iterative approach, soliciting a great deal of user feedback.
- Develop a way to measure the value of the intranet site in terms of reduced costs and new revenues, both during the project and one year after project completion.

ROLES AND RESPONSIBILITIES (PARTIAL LIST)

Name	Role	Position	Contact Information
Joe Fleming	Sponsor	JWD Consulting, CEO	joe_fleming@jwdconsulting.com
Erica Bell	Project Manager	JWD Consulting, manager	erica_bell@jwdconsulting.com
Michael Chen	Team Member	JWD Consulting, senior consultant	michael_chen@jwdconsulting.com
Jessie Faue	Team Member	JWD Consulting, consultant	jessie_faue@jwdconsulting.com
Kevin Dodge	Team Member	JWD Consulting, IT department	kevin_dodge@jwdconsulting.com
Cindy Dawson	Team Member	JWD Consulting, IT department	cindy_dawson@jwdconsulting.com
Kim Phuong	Advisor	Client representative	kim_phuong@client1.com
Page Miller	Advisor	Client representative	page_miller@client2.com

Sign-Off: (Signatures of all the above stakeholders)
Comments: (Handwritten or typed comments from above stakeholders, if applicable)

"I will support this project as time allows, but I believe my client projects take priority. I will have one of my assistants support the project as needed."—Michael Chen

"We need to be extremely careful—testing this new system, especially the security in giving access to parts of the intranet site to the public and clients."—Kevin Dodge and Cindy Dawson

Project Planning

1. Planning processes and outputs

TABLE 3-7 Planning processes and outputs

Knowledge Area	Planning Process	Outputs
Project Integration Management	Develop project management plan	Project management plan
Project Scope Management	Plan scope management	Scope management plan Requirements management plan
	Collect requirements	Requirements documentation Requirements traceability matrix
	Define scope	Project scope statement Project documents updates
	Create WBS	Scope baseline Project documents updates
Project Schedule Management	Plan schedule management	Schedule management plan

(continued)

TABLE 3-7 Planning processes and outputs (*continued*)

Knowledge Area	Planning Process	Outputs
	Define activities	Activity list Activity attributes Milestone list Change requests Project management plan updates
	Sequence activities	Project schedule network diagrams Project documents updates
	Estimate activity durations	Activity duration estimates Basis of estimates Project documents updates
	Develop schedule	Schedule baseline Project schedule Schedule data Project calendars Project management plan updates Project documents updates

Project Cost Management	Plan cost management	Cost management plan
	Estimate costs	Cost estimates Basis of estimates Project documents updates
	Determine budget	Cost baseline Project funding requirements Project documents updates
Project Quality Management	Plan quality management	Quality management plan Quality metrics Project management plan updates Project documents updates
Project Resource Management	Plan resource management Estimate activity resources	Resource management plan Team charter Project document updates Resource requirements Basis of estimates Resource breakdown structure Project documents updates
Project Communications Management	Plan communications management	Communications management plan Project management plan updates Project documents updates

(*continued*)

TABLE 3-7 Planning processes and outputs (*continued*)

Knowledge Area	Planning Process	Outputs
Project Risk Management	Plan risk management	Risk management plan
	Identify risks	Risk register Risk report
	Perform qualitative risk analysis	Project documents updates
	Perform quantitative risk analysis	Project documents updates Change requests
	Plan risk responses	Project management plan updates Project documents updates
Project Procurement Management	Plan procurement management	Procurement management plan Procurement strategy Bid documents Procurement statement of work Source selection criteria Make or buy decisions Independent cost estimates Change requests Project documents updates Organizational process assets updates
Project Stakeholder Management	Plan stakeholder engagement	Stakeholder engagement plan

Source: *PMBOK® Guide – Sixth Edition*, 2017.

2. Team charter

TABLE 3-8 Team charter

Code of Conduct: As a project team, we will:

- Work proactively, anticipating potential problems and working to prevent them.
- Keep other team members informed of information related to the project.
- Focus on what is best for the entire project team.

Participation: We will:

- Be honest and open during all project activities.
- Encourage diversity in team work.
- Provide the opportunity for equal participation.
- Be open to new approaches and consider new ideas.
- Have one discussion at a time.
- Let the project manager know well in advance if a team member has to miss a meeting or may have trouble meeting a deadline for a given task.

Communication: We will:

- Decide as a team on the best way to communicate. Because a few team members cannot often meet face to face, we will use e-mail, a project website, and other technology to assist in communicating.
- Have the project manager facilitate all meetings and arrange for phone and video conferences, as needed.
- Work together to create the project schedule and enter actuals into the enterprise-wide project management system by 4 p.m. every Friday.
- Present ideas clearly and concisely.
- Keep discussions on track.

Problem Solving: We will:

- Encourage everyone to participate in solving problems.
- Only use constructive criticism and focus on solving problems, not blaming people.
- Strive to build on each other's ideas.

Meeting Guidelines: We will:

- Have a face-to-face meeting the first and third Tuesday morning of every month.
- Meet more frequently the first month.
- Hold other meetings as needed.
- Record meeting minutes and send them via e-mail within 24 hours of all project meetings, focusing on decisions made and action items from each meeting.

3. Project scope statement

TABLE 3-9 Scope statement draft

Project Title: Project Management Intranet Site Project
Date: May 18 **Prepared by:** Erica Bell, Project Manager, erica_bell@jwdconsulting.com

Project Summary and Justification: Joe Fleming, CEO of JWD Consulting, requested this project to assist the company in meeting its strategic goals. The new intranet site will increase visibility of the company's expertise to current and potential clients. It will also help reduce internal costs and improve profitability by providing standard tools, techniques, templates, and project management knowledge to all internal consultants. The budget for the project is $140,000. An additional $40,000 per year will be required for operational expenses after the project is completed. Estimated benefits are $200,000 each year. It is important to focus on the system paying for itself within one year of its completion.

Product Characteristics and Requirements:

1. **Templates and tools:** The intranet site will allow authorized users to download files they can use to create project management documents and to help them use project management tools. These files will be in Microsoft Word, Excel, Access, Project, or in HTML or PDF format, as appropriate.
2. **User submissions:** Users will be encouraged to e-mail files with sample templates and tools to the Webmaster. The Webmaster will forward the files to the appropriate person for review and then post the files to the intranet site, if desired.
3. **Articles:** Articles posted on the intranet site will have appropriate copyright permission. The preferred format for articles will be PDF. The project manager may approve other formats.
4. **Requests for articles:** The intranet site will include a section for users to ask someone from the Project Management Office (PMO) at JWD Consulting to research appropriate articles for them. The PMO manager must first approve the request and negotiate payments, if appropriate.

(*continued*)

TABLE 3-9 Scope statement draft (*continued*)

5. Links: All links to external sites will be tested on a weekly basis. Broken links will be fixed or removed within five working days of discovery.
6. The Ask the Expert feature must be user-friendly and capable of soliciting questions and immediately acknowledging that the question has been received in the proper format. The feature must also be capable of forwarding the question to the appropriate expert (as maintained in the system's expert database) and capable of providing the status of questions that are answered. The system must also allow for payment for advice, if appropriate.
7. Security: The intranet site must provide several levels of security. All internal employees will have access to the entire intranet site when they enter their security information to access the main, corporate intranet. Part of the intranet will be available to the public from the corporate website. Other portions of the intranet will be available to current clients based on verification with the current client database. Other portions of the intranet will be available after negotiating a fee or entering a fixed payment using pre-authorized payment methods.
8. Search feature: The intranet site must include a search feature for users to search by topic and key words.
9. The intranet site must be accessible using a company-approved Internet browser. Users must have appropriate application software to open several of the templates and tools.
10. The intranet site must be available 24 hours a day, 7 days a week, with one hour per week for system maintenance and other periodic maintenance, as appropriate.

Summary of Project Deliverables

Project management–related deliverables: Business case, project charter, team charter, scope statement, WBS, schedule, cost baseline, progress reports, final project presentation, final project report, lessons-learned report, and any other documents required to manage the project.

Product-related deliverables:

1. Survey: Survey current consultants and clients to help determine desired content and features for the intranet site.
2. Files for templates: The intranet site will include templates for at least 20 documents when the system is first implemented, and it will have the capacity to store up to 100 documents. The project team will decide on the initial 20 templates based on survey results.
3. Examples of completed templates: The intranet site will include examples of projects that have used the templates available on the site. For example, if there is a template for a business case, there will also be an example of a real business case that uses the template.

(*continued*)

TABLE 3-9 Scope statement draft (*continued*)

4. Instructions for using project management tools: The intranet site will include information on how to use several project management tools, including the following as a minimum: work breakdown structures, Gantt charts, network diagrams, cost estimates, and earned value management. Where appropriate, sample files will be provided in the application software appropriate for the tool. For example, Microsoft Project files will be available to show sample work breakdown structures, Gantt charts, network diagrams, cost estimates, and applications of earned value management. Excel files will be available for sample cost estimates and earned value management charts.
5. Example applications of tools: The intranet site will include examples of real projects that have applied the tools listed in number 4.
6. Articles: The intranet site will include at least 10 useful articles about relevant topics in project management. The intranet site will have the capacity to store at least 1,000 articles in PDF format with an average length of 10 pages each.
7. Links: The intranet site will include links with brief descriptions for at least 20 useful sites. The links will be categorized into meaningful groups.
8. Expert database: In order to deliver an Ask the Expert feature, the system must include and access a database of approved experts and their contact information. Users will be able to search for experts by predefined topics.
9. User Requests feature: The intranet site will include an application to solicit and process requests from users.
10. Intranet site design: An initial design of the new intranet site will include a site map, suggested formats, and appropriate graphics. The final design will incorporate comments from users on the initial design.
11. Intranet site content: The intranet site will include content for the templates and tools sections, articles section, article retrieval section, links section, Ask the Expert section, User Requests feature, security, and payment features.
12. Test plan: The test plan will document how the intranet site will be tested, who will do the testing, and how bugs will be reported.
13. Promotion: A plan for promoting the intranet site internally and externally will describe various approaches for soliciting inputs during design. The promotion plan will also announce the availability of the new intranet site.
14. Project benefit measurement plan: A project benefit plan will measure the financial value of the intranet site.

Project Success Criteria: Our goal is to complete this project within six months for no more than $140,000. The project sponsor, Joe Fleming, has emphasized the importance of the project paying for itself within one year after the site is complete. To meet this financial goal, the intranet site must have strong user inputs. We must also develop a method for capturing the benefits while the intranet site is being developed and tested, and after it is rolled out. If the project takes a little longer to complete or costs a little more than planned, the firm will still view it as a success if it has a good payback and helps promote the firm's image as an excellent consulting organization.

4. Work breakdown structure (WBS) by process group

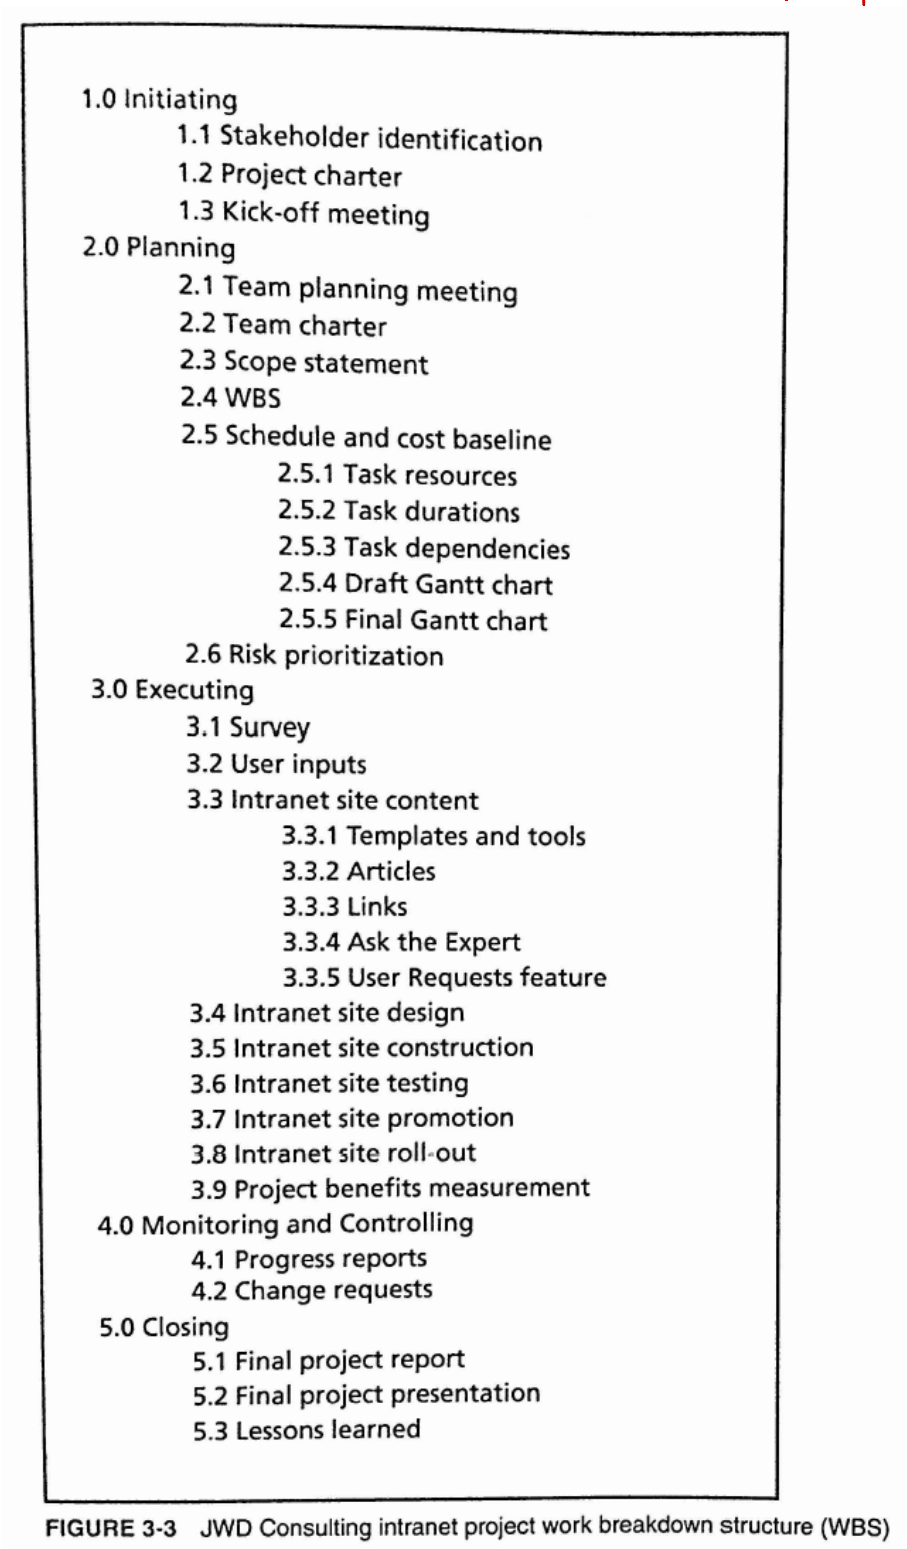


FIGURE 3-3 JWD Consulting intranet project work breakdown structure (WBS)

Project Execution

1. Executing processes and outputs

TABLE 3-11 Executing processes and outputs

Knowledge Area	Executing Process	Outputs
Project Integration Management	Direct and manage project work	Deliverables Work performance data Issue log Change requests Project management plan updates Project documents updates Organizational process assets updates
	Manage project knowledge	Lessons-learned register Project management plan updates Organizational process assets updates
Project Quality Management	Manage quality	Quality report Test and evaluation documents Change requests Project management plan updates Project documents updates
Project Resource Management	Acquire resources	Physical resource assignments Project team assignments Resource calendars Change requests Project management plan updates Project documents updates Enterprise environmental factors updates Organizational process assets updates Team performance assessments
	Develop team	Change requests Project management plan updates Project documents updates Enterprise environmental factors updates Organizational process assets updates
	Manage team	Change requests Project management plan updates Project documents updates Enterprise environmental factors updates
Project Communications Management	Manage communications	Project communications Project management plan updates Project documents updates Organizational process assets updates

TABLE 3-11 Executing processes and outputs (*continued*)

Knowledge Area	Executing Process	Outputs
Project Risk Management	Implement risk responses	Change requests Project documents updates
Project Procurement Management	Conduct procurements	Selected sellers Agreements Change requests Project management plan updates Project documents updates Organizational process assets updates
Project Stakeholder Management	Manage stakeholder engagement	Change requests Project management plan updates Project documents updates Organizational process assets updates

Source: *PMBOK® Guide – Sixth Edition*, 2017.

2. Milestone report

TABLE 3-12 Milestone report as of June 17

Milestone	Date	Status	Responsible	Issues/ Comments
Initiating Stakeholders identified	May 2	Completed	Erica and Joe	
Project charter signed	May 10	Completed	Erica	
Project kick-off meeting held	May 13	Completed	Erica	Went very well
Planning Team charter signed	May 13	Completed	Erica	
Scope statement completed	May 27	Completed	Erica	
WBS completed	May 31	Completed	Erica	
List of prioritized risks completed	June 3	Completed	Erica	Reviewed with sponsor and team
Schedule and cost baseline completed	June 13	Completed	Erica	
Executing Survey and analysis completed	June 28		Erica	Poor response so far!
Intranet site design completed	July 26		Kevin	
Project benefits measurement completed	August 9		Erica	
User inputs collected	August 9		Jessie	
Articles completed	August 23		Jessie	
Templates and tools completed	September 6		Erica	
Ask the Expert completed	September 6		Michael	

(continued)

TABLE 3-12 Milestone report as of June 17 (*continued*)

Milestone	Date	Status	Responsible	Issues/ Comments
User Requests feature completed	September 6		Cindy	
Links completed	September 13		Kevin	
Intranet site construction completed	October 4		Kevin	
Intranet site testing completed	October 18		Cindy	
Intranet site promotion completed	October 25		Erica	
Intranet site roll-out completed	October 25		Kevin	
Monitoring and Controlling Progress reports	Every Friday		All	
Closing				
Final project presentation completed	October 27		Erica	
Sponsor sign-off on project completed	October 27		Joe	
Final project report completed	October 28		Erica	
Lessons-learned reports submitted	November 1		All	

Project Monitoring and Controlling

1. Monitoring and controlling processes and outputs

TABLE 3-13 Monitoring and controlling processes and outputs

Knowledge Area	Monitoring and Controlling Process	Outputs
Project Integration Management	Monitor and control project work	Work performance reports Change requests Project management plan updates Project documents updates
	Perform integrated change control	Approved change requests Project management plan updates Project documents updates
Project Scope Management	Validate scope	Accepted deliverables Work performance information Change requests Project documents updates
	Control scope	Work performance information Change requests Project management plan updates Project documents updates
Project Schedule Management	Control schedule	Work performance information Schedule forecasts Change requests Project management plan updates Project documents updates
Project Cost Management	Control cost	Work performance information Cost forecasts Change requests Project management plan updates Project documents updates
Project Quality Management	Control quality	Quality control measurements Verified deliverables Work performance information Change requests Project management plan updates Project documents updates
Project Resource Management	Control resources	Work performance information Change requests Project management plan updates Project documents updates

(*continued*)

TABLE 3-13 Monitoring and controlling processes and outputs (*continued*)

Knowledge Area	Monitoring and Controlling Process	Outputs
Project Communications Management	Monitor communications	Work performance information Change requests Project management plan updates Project documents updates
Project Stakeholder Management	Monitor stakeholder engagement	Work performance information Change requests Project management plan updates Project documents updates
Project Risk Management	Monitor risks	Work performance information Change requests Project management plan updates Project documents updates Organizational process assets updates
Project Procurement Management	Control procurements	Closed procurements Work performance information Procurement documentation updates Change requests Project management plan updates Project documents updates Organizational process assets updates

Source: *PMBOK® Guide – Sixth Edition*, 2017.

2. Weekly progress report

TABLE 3-14 Sample weekly progress report

Project Name: Project Management Intranet Project
Team Member Name: Cindy Dawson, cindy_dawson@jwdconsulting.com
Date: August 5

Work completed this week:

–Worked with Kevin to start the intranet site construction
–Organized all the content files
–Started developing a file naming scheme for content files
–Continued work on Ask the Expert and User Requests features
–Met with preferred supplier
–Verified that their software would meet our needs
–Discovered the need for some customization

Work to complete next week:

–Continue work on intranet site construction
–Prepare draft contract for preferred supplier
–Develop new cost estimate for outsourced work

What's going well and why:

The intranet site construction started well. The design was very clear and easy to follow. Kevin really knows what he's doing.

What's not going well and why:

It is difficult to decide how to organize the templates and examples. Need more input from senior consultants and clients.

Suggestions/Issues:

–Hold a special meeting to decide how to organize the templates and examples on the intranet site.
–Get some sample contracts and help in negotiating with the preferred supplier.

Project changes:

I think we can stay on schedule, but it looks like we'll need about $10,000 more for outsourcing. That's doubling our budget in that area.

Project Closing

1. Lesson learned report (partial)

TABLE 3-16 Lessons-learned report (abbreviated)

Project Name:	JWD Consulting Project Management Intranet Site Project
Project Sponsor:	Joe Fleming
Project Manager:	Erica Bell
Project Dates:	May 2–November 4
Final Budget:	$150,000

1. Did the project meet scope, time, and cost goals?

   We did meet scope and time goals, but we had to request an additional $10,000, which the sponsor approved.

2. What were the success criteria listed in the project scope statement?

   Below is what we put in our project scope statement under project success criteria:

   "Our goal is to complete this project within six months for no more than $140,000. The project sponsor, Joe Fleming, has emphasized the importance of the project paying for itself within one year after the intranet site is complete. To meet this financial goal, the intranet site must have strong user input. We must also develop a method for capturing the benefits while the intranet site is being developed and tested, and after it is rolled out. If the project takes a little longer to complete or costs a little more than planned, the firm will still view it as a success if it has a good payback and helps promote the firm's image as an excellent consulting organization."

(*continued*)

TABLE 3-16 Lessons-learned report (abbreviated) (*continued*)

3. Reflect on whether you met the project success criteria.

   As stated above, the sponsor was not too concerned about going over budget as long as the system would have a good payback period and help promote the firm's image. We have already documented some financial and image benefits of the new intranet site. For example, we have decided that we can staff the PMO with one less person, resulting in substantial cost savings. We have also received excellent feedback from several of our clients about the new intranet site.

4. What were the main lessons your team learned from managing this project?

   The main lessons we learned include the following:

   - *Having a good project sponsor was instrumental to project success. We ran into a couple of difficult situations, and Joe was very creative in helping us solve problems.*
   - *Teamwork was essential. It really helped to take time for everyone to get to know each other at the kick-off meeting. It was also helpful to develop and follow a team charter.*
   - *Good planning paid off in execution. We spent a fair amount of time developing a good project charter, scope statement, WBS, schedules, and so on. Everyone worked together to develop these planning documents, and there was strong buy-in.*
   - *Project management software was very helpful throughout the project.*

5. Describe one example of what went right on this project.

6. Describe one example of what went wrong on this project.

7. What will you do differently on the next project based on your experience working on this project?

2. Final project report table of contents

TABLE 3-17 Final project report table of contents

1. Project Objectives
2. Summary of Project Results
3. Original and Actual Start and End Dates
4. Original and Actual Budget
5. Project Assessment (Why did you do this project? What did you produce? Was the project a success? What went right and wrong on the project?)
6. Transition Plan
7. Annual Project Benefits Measurement Approach

Attachments: deliverables

A Project Management Documentation

- Business case
- Project charter
- Team charter
- Scope statement
- WBS and WBS dictionary
- Baseline and actual Gantt chart
- List of prioritized risks
- Milestone reports
- Progress reports
- Contract files
- Lessons-learned reports
- Final presentation
- Client acceptance form

B Product-Related Documentation

- Survey and results
- Summary of user inputs
- Intranet site content
- Intranet site design documents
- Test plans and reports
- Intranet site promotion information
- Intranet site roll-out information
- Project benefits measurement information

Templates by Process Group

TABLE 3-20 Templates by process group

Template Name	Process Group	Chapter(s) Where Used	Application Software	File Name
Business Case	Pre-initiating	3	Word	business case.doc
Business Case Financials	Pre-initiating	3, 4	Excel	business case financials.xls
Stakeholder Register	Initiating	3, 13	Word	stakeholder register.doc

(*continued*)

TABLE 3-20 Templates by process group (*continued*)

Template Name	Process Group	Chapter(s) Where Used	Application Software	File Name
Stakeholder Management Strategy	Initiating	3, 13	Word	stakeholder management strategy.doc
Kick-off Meeting Agenda	Initiating	3	Word	kick-off meeting agenda.doc
Payback Period Chart	Initiating	4	Excel	payback period chart.xls
Weighted Scoring Model	Initiating	4, 12	Excel	weighted scoring model.xls
Project Charter	Initiating	3, 4, 5	Word	charter.doc
Assumption Log	Initiating	3, 4	Excel	assumption log.xlsx
Team Charter	Planning	3, 9	Word	team charter.doc
Requirements Traceability Matrix	Planning	5	Word	requirements traceability matrix.doc
Scope Statement	Planning	3, 4, 5	Word	scope statement.doc
Contract Statement of Work	Planning	12	Word	contract statement of work.doc
Request for Proposal	Planning	12	Word	request for proposal.doc
Project Management Plan	Planning	4	Word	project management plan.doc
Work Breakdown Structure (WBS)	Planning	3, 5, 6	Word	wbs.doc
WBS Dictionary Entry	Planning	5		WBS dictionary description.doc
Cost Estimate	Planning	7	Excel	cost estimate.xls
Earned Value Chart	Monitoring and Controlling	7	Excel	earned value chart.xls

(*continued*)

TABLE 3-20 Templates by process group (*continued*)

Template Name	Process Group	Chapter(s) Where Used	Application Software	File Name
Burndown Chart	Monitoring and Controlling	3, 7	Excel	burndownchart.xls
Quality Metrics	Executing	8	Word	quality metrics.doc
Pareto Chart	Monitoring and Controlling	8	Excel	pareto chart.xls
Project Organizational Chart	Planning, Executing	9	PowerPoint	project organizational chart.ppt
Responsibility Assignment Matrix	Planning, Executing	9	Excel	RACI chart.xls
Resource Histogram	Planning, Executing	9	Excel	resource histogram.xls
Communications Management Plan	Planning	10	Word	communications managemnt plan.doc
Lessons-learned Register	Executing	4	Excel	lessons-learned register.xlsx
Milestone Report	Executing	3, 6	Word	milestone report.doc
Change Request Form	Planning, Monitoring and Controlling	4	Word	change request.doc
Performance Report	Monitoring and Controlling	3, 4	Word	performance report.doc
Probability/ Impact Matrix	Planning, Executing, Monitoring and Controlling	11	PowerPoint	probability impact matrix.ppt
Risk Register	Planning, Monitoring and Controlling	11	Excel	risk register.xls
Breakeven/Sensitivity Analysis	Planning	11	Excel	breakeven.xls

(*continued*)

TABLE 3-20 Templates by process group (*continued*)

Template Name	Process Group	Chapter(s) Where Used	Application Software	File Name
Contract	Planning	12	Word	contract.doc
Request for Proposal	Planning	12	Word	request for proposal .doc
Issue Log	Monitoring and Controlling	13	Word	issue log.doc
Customer Acceptance Form	Closing	10	Word	customer acceptance form.doc
Lessons-Learned Report	Closing	3, 10	Word	lessons-learned report.doc
Final Project Report Table of Contents	Closing	3, 10	Word	final project report table of contents.doc
