Chapter 3: The Project Management Process Groups

Information Technology Project Management, Ninth Edition

Note: See the text itself for full citations

Twittie Senivongse (ed.)

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Learning Objectives

- Describe the five project management process groups, the typical level of activity for each, and the interactions among them
- Relate the project management process groups to the project management knowledge areas
- Review a case study of an organization applying the project management process groups to manage an IT project and describe outputs of each process group
- Review a case study of the same project managed compare the key differences between a predictive approach and an agile approach
- Describe several templates for creating documents for each process group

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Management Process Groups (1 of 2)

- A process is a series of actions directed toward a particular result
  - Project management can be viewed as a number of related processes
- Project management process groups
  - Initiating processes
  - Planning processes
  - Executing processes
  - Monitoring and controlling processes
  - Closing processes

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Management Process Groups (1 of 4)

- Initiating processes
  - Defining and authorizing a project or project phase
  - Identifying stakeholders
  - E.g. In finishing phase, ensuring that the team completes all work, someone documents lessons learned, relevant stakeholders are prepared
- Planning processes
  - Devising and maintaining a workable scheme, e.g. scope/schedule/cost/procurement management plans
  - Revising plans during each phase to account for changing conditions
- Executing processes
  - Coordinating people and other resources to carry out plans
  - Creating products, services, or results of the project or phase
  - E.g. managing project work, managing project knowledge, acquiring resources, conducting procurements

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Management Process Groups (2 of 4)

- Monitoring and controlling processes
  - Monitoring and measuring progress against plans
  - Taking corrective actions when necessary
  - E.g. reporting performance, identifying necessary changes
- Closing processes
  - Formalizing acceptance of the project or project phase and ending it
  - E.g. archiving project files, documenting lessons learned, receiving formal acceptance of the delivered work


Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Management Process Groups (3 of 4)

- Process groups are not mutually exclusive
  - E.g. monitoring and controlling occurs concurrently with other process groups throughout the project
- Level of activity and length of each process group varies for every project
  - Executing normally requires the most resources and time, followed by planning
- Process groups can be applied to an entire project (i.e. waterfall) or to each phase or iteration of a project (i.e. agile)

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Management Process Groups (4 of 4)

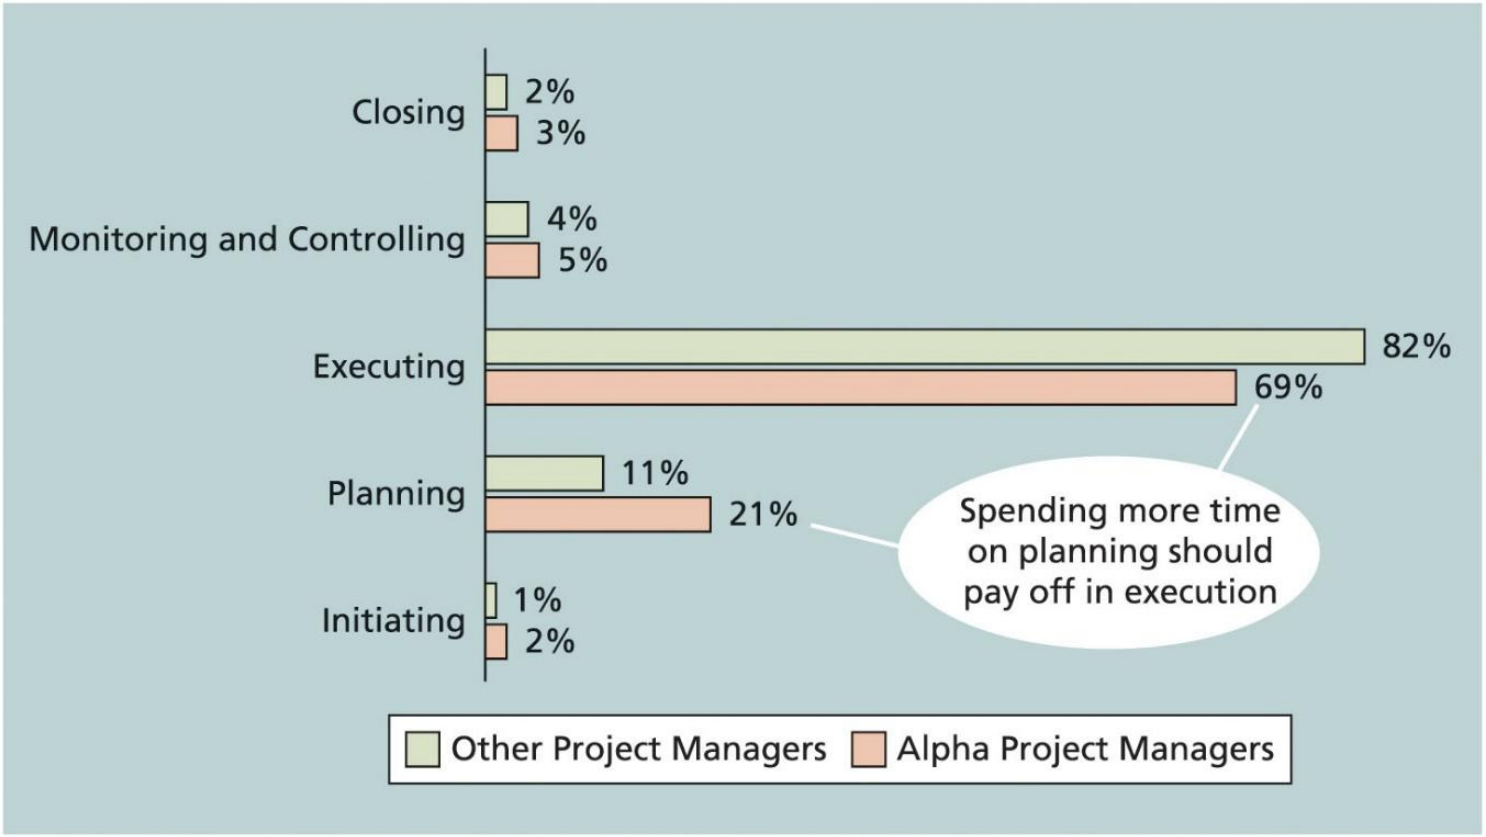

Source: Andy Crowe

FIGURE 3-1 Percentage of time spent on each process group

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Mapping the Process Groups to the Knowledge Areas

- You can map the main activities of each PM process group into the ten knowledge areas using the *PMBOK® Guide, Sixth Edition*
  - Note that there are activities from each knowledge area under the planning process groups

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Knowledge Area	Project Management Process Groups				
	Initiating Process Group	Planning Process Group	Executing Process Group	Monitoring and Controlling Process Group	Closing Process Group
4. *Project Integration Management*	4.1 Develop Project Charter	4.2 Develop Project Management Plan	4.3 Direct and Manage Project Work 4.4 Manage Project Knowledge	4.5 Monitor and Control Project Work 4.6 Perform Integrated Change Control	4.7 Close Project or Phase
5. *Project Scope Management*		5.1 Plan Scope Management 5.2 Collect Requirements 5.3 Define Scope 5.4 Create WBS		5.5 Validate Scope 5.6 Control Scope	
6. *Project Schedule Management*		6.1 Plan Schedule Management 6.2 Define Activities 6.3 Sequence Activities 6.4 Estimate Activity Durations 6.5 Develop Schedule		6.6 Control Schedule	
7. *Project Cost Management*		7.1 Plan Cost Management 7.2 Estimate Costs 7.3 Determine Budget		7.4 Control Costs	

Knowledge Area	Project Management Process Groups: Initiating Process Group	Planning Process Group	Executing Process Group	Monitoring and Controlling Process Group	Closing Process Group
8. Project Quality Management		8.1 Plan Quality Management	8.2 Manage Quality	8.3 Control Quality	
9. Project Resource Management		9.1 Plan Resource Management 9.2 Estimate Activity Resources	9.3 Acquire Resources 9.4 Develop Team 9.5 Manage Team	9.6 Control Resources	
10. Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 Monitor Communications	
11. Project Risk Management		11.1 Plan Risk Management 11.2 Identify Risks 11.3 Perform Qualitative Risk Analysis 11.4 Perform Quantitative Risk Analysis 11.5 Plan Risk Responses	11.6 Implement Risk Responses	11.7 Monitor Risks	
12. Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
13. Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder Engagement	13.3 Manage Stakeholder Engagement	13.4 Monitor Stakeholder Engagement	

How are they different?



Product life cycle, e.g. SDLC (waterfall, agile, etc.)

Project life cycle

Starting the project	Organizing and preparing	Carrying out the work	Finishing the project

Process groups

Initiating	Planning	Executing	Monitoring and controlling	Closing

Knowledge areas

Integration Mgt	Scope Mgt	Schedule Mgt	Cost Mgt	Resource Mgt	Quality Mgt	Risk Mgt	Communication Mgt	Procurement Mgt	Stakeholder Mgt

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Case Study: JWD Consulting's Project Management Intranet Site

- JWD Consulting assists organizations in managing IT projects
- Joe Fleming, CEO, wanted his company to become world-class consulting organization
- He asked Erica Bell, Director of Project Management Office (PMO), and her team to develop an intranet site to share their project management knowledge
  - Provide templates, tools, articles, and links to other sites for staff as well as clients
  - Ask the Expert feature to help build relationships with current and future clients

Joe 

Erica 

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Icon made by Freepik from www.flaticon.com

Case Study 1: JWD Consulting's Project Management Intranet Site (Predictive Approach)

- This case study provides an example of what's involved in initiating, planning, executing, monitoring and controlling, and closing an IT project
- Note: this case study provides a big picture view of managing a project
  - Later chapters provide detailed information on each knowledge area

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Pre-initiation (1 of 3)

- Strategic planning (vision, mission, goals) should serve as the foundation for deciding which projects to pursue
- JWD's goal is to provide consulting services more effectively and efficiently
- Developing the intranet site could
  - Reduce internal cost by working more effectively
  - Allow existing and potential customers to access information
  - Increase revenue by bringing in more business

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Pre-initiation (2 of 3)

- It is good practice to lay the groundwork for a project before it officially starts
- Senior managers often perform several pre-initiation tasks



Pre-initiation Tasks	JWD
Determine the scope, time, and cost constraints for the project	Scope: Provide templates, tools, articles, and links to other sites for staff as well as clients, Ask the Expert feature Time: 6 months Cost: To be determined
Identify the project sponsor	Joe Fleming
Select the project manager	Erica Bell
Develop a business case for a project	Drafted by Erica
Meet with the project manager to review the process and expectations for managing the project	Done
Determine if the project should be divided into two or more smaller projects (easier for smaller projects to succeed)	No, small project

Pre-initiation (3 of 3)

- Business case
  - Drafted by Erica after getting input and feedback from Joe, a senior PMO staff member, and a Finance Department staff member
  - Topics include
    - Introduction/background
    - Business objective
    - Current situation and problem/opportunity statement
    - Critical assumptions and constraints
    - Analysis of options and recommendation
    - Preliminary project requirements
    - Budget estimate and financial analysis
    - Schedule estimate
    - Potential risks
    - Exhibits
  - See attachment document





Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Icon made by Smashicons from www.flaticon.com

Project Initiation (1 of 5)

- Initiating includes recognizing and starting a new project

Knowledge Area	Initiating Process	Outputs
Project Integration Management	Develop project charter	Project charter Assumption log
Project Stakeholder Management	Identify stakeholders	Stakeholder register Change requests Project management plan updates Project documents updates

Source: PMBOK® Guide – Sixth Edition, 2017

Table 3-3 Project initiation knowledge areas, processes, and outputs



LOTR project management concept https://www.youtube.com/watch?v=UIVWaUgqEAc

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Initiation (2 of 5)



Name	Position	Internal/ External	Project Role	Contact Information
Joe Fleming	CEO	Internal	Sponsor	joe_fleming@jwdconsulting.com
Erica Bell	PMO Director	Internal	Project Manager	erica_bell@jwdconsulting.com
Michael Chen	Senior Consultant	Internal	Team Member	michael_chen@jwdconsulting.com
Cindy Dawson	IT	Internal	Team Member	cindy_dawson@jwdconsulting.com
Kim Phuong	Business Analyst	External	Advisor	kim_phuong@client1.com
Louise Mills	PR Director	Internal	Advisor	louise_mills@jwdconsulting.com
…				

Table 3-4 Stakeholder Register (partial)

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Initiation (3 of 5)



- Stakeholder management strategy can accompany the stakeholder register to record info for gaining support or reduce obstacles from each stakeholder
- Sensitive and kept confidential (or not written down at all)

Name	Level of Interest	Level of Influence	Potential Management Strategies
Joe Fleming	High	High	Joe likes to stay on top of key projects and make money. Have a lot of short, face-to-face meetings and focus on achieving the financial benefits of the project.
Louise Mills	Low	High	Louise has a lot of things on her plate, and she does not seem excited about this project. She may be looking at other job opportunities. Show her how this project will help the company and her resume.

Table 3-5 Stakeholder Management Strategy

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Initiation (4 of 5)






- Drafting the project charter
  - JWD has it 1-2 pages long and may refer to other documents (e.g. business case)
  - Has it signed by all stakeholders and also record their comments
  - See attachment document



- Holding a project kick-off meeting
  - Good practice at the beginning of a project, so that stakeholders can meet each other, review the goals of the project, and discuss future plans
  - Some or all stakeholders may meet virtually
  - Prepare meeting agenda – meeting objective, agenda, action items, assigned to, due date, next meeting
  - Document meeting minutes and send to all within 1-2 days after meeting



Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Icon made by Freepik from www.flaticon.com

Project Initiation (5 of 5)

Kick-Off Meeting
[Date of Meeting]

Project Name: Project Management Intranet Site Project

Meeting Objective: Get the project off to an effective start by introducing key stakeholders, reviewing project goals, and discussing future plans

Agenda:

- Introductions of attendees
- Review of the project background
- Review of project-related documents (business case and project charter)
- Discussion of project organizational structure
- Discussion of project scope, time, and cost goals
- Discussion of other important topics
- List of action items from meeting

Action Item	Assigned To	Due Date

Date and time of next meeting:

FIGURE 3-2 Kick-off meeting agenda

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (1 of 6)

- The main purpose is to guide execution
- Often the most difficult process, and fair amount of time and effort must go into planning
- Plans must be realistic and useful
- People who know about the work need to plan the work
- Every knowledge area includes planning information
  - See attachment document 
- Key outputs included in the JWD project
  - Team charter
  - Project scope statement
  - Work breakdown structure (WBS)
  - Project schedule, in the form of a Gantt chart
  - Resource and cost info
  - List of prioritized risks (part of a risk register)
  - Also, prepare project web site to house project documents

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (2 of 6)



- Meetings with project team
  - Team building activity in the first meeting helps the team members to get to know each other
  - Erica and Jessie prepared documents for team to review and discuss

- Team charter
  - Help promote teamwork and clarify team communications
  - Have the team share ideas about what should be in the team charter
  - See attachment document

- Project scope statement
  - Given the high-level project requirements, budget estimate, and schedule estimate in the project charter, have the team share ideas about
    - What should be the main deliverables
    - Any unclear points in the scope or foreseen issues
  - See attachment document

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (3 of 6)





- Work breakdown structure (WBS)
  - Prepared along with the scope statement
  - Basis for deciding how to do the work and for creating project schedule
  - May use the process groups as the categories of work
  - See attachment document



- Project schedule (Gantt chart)
  - While discussing the scope and deliverable, Erica also asked team members
    - Which task or deliverables the team members would help create or review
    - Number of hours the team members would work each month during the project
  - Given the high-level project requirements, budget estimate, and schedule estimate in the project charter, Erica and the team
    - Determined task dependency
    - Estimated the number of hours on each task and task duration
    - If necessary, determined critical path and adjusted schedule to fit the schedule goal

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (4 of 6)

Baseline schedule with task dependency, milestones, and process groups in linear pattern, resulting in one release

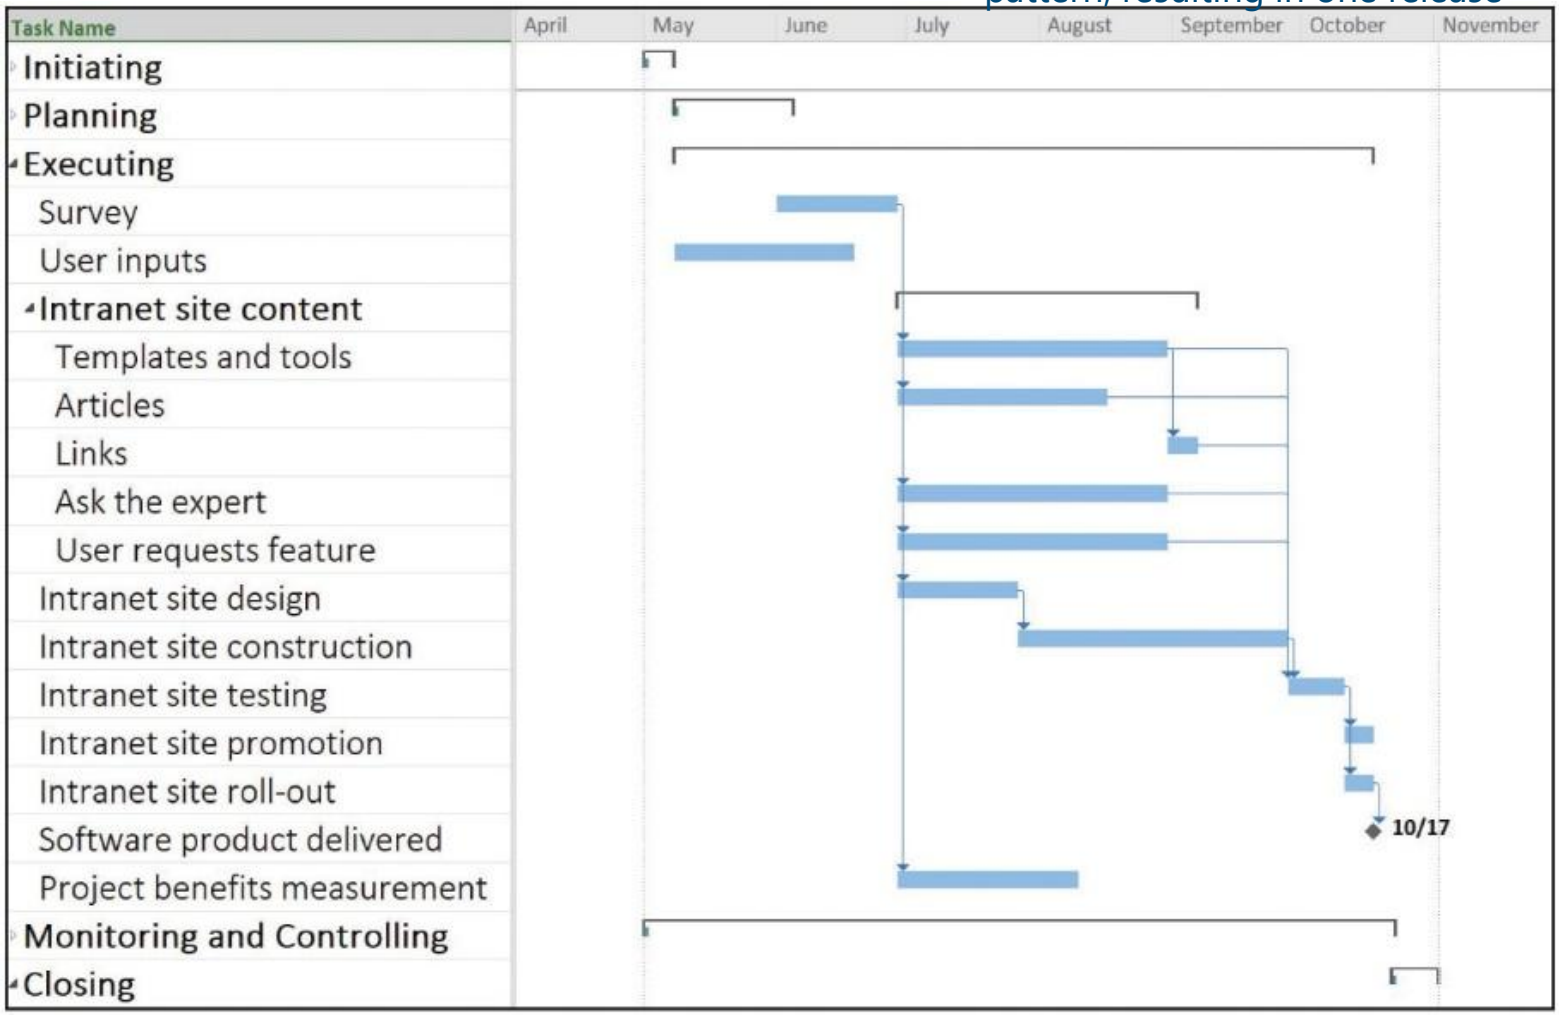


FIGURE 3-4 JWD Consulting intranet site project baseline Gantt chart

Project

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (5 of 6)



- Resource and cost info
  - Given the scope, budget estimate, and schedule estimate in the WBS and project charter, prepare
    - Labor rate and labor cost of each team member
    - Procurement cost of external software and services

- List of prioritized risks
  - Given the potential risks and member comments in the project charter, have the team
    - Discuss risks
    - Determine probability of each risk (high, medium, low)
    - Determine impact of each risk (high, medium, low)
    - Prioritize risks

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (6 of 6)

Ranking	Potential Risk
1	Lack of inputs from internal consultants
2	Lack of inputs from client representatives
3	Security of new system
4	Outsourcing/purchasing for the article retrieval and Ask the Expert features
5	Outsourcing/purchasing for processing online payment transactions
6	Organizing the templates and examples in a useful fashion
7	Providing an efficient search feature
8	Getting good feedback from Michael Chen and other senior consultants
9	Effectively promoting the new system
10	Realizing the benefits of the new system within one year

Table 3-10 List of Prioritized Risks

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.


Project Execution (1 of 2)

- Taking actions to complete the tasks in the project plan and create the products
- Usually takes the most resources to perform
  - See attachment document for knowledge areas, executing processes, and outputs of project execution



- Many project sponsors and customers focus on deliverables related to providing the products, services, or results
  - It is equally important to document change requests and update planning documents
- A milestone report can help focus on completing major milestones
  - Erica worked closely with all members to ensure they were completing the desired work results, and reviewed with Joe once a week
  - See attachment document









Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Execution (2 of 2)

- Project managers must use their leadership skills to handle the many challenges that occur during project execution
  - Adjust communication style with team members
    - Working on other client projects, Michael was too busy for meetings. Erica agreed to have him attend minimal number of project meetings, provided that he was contributing to the Ask the Expert feature
  - Handle conflict
    - Kevin wanted to write all software himself, but Cindy thought it was better to buy software for the Ask the Expert and User Requests features. Erica agreed with Cindy and had to convince Kevin
  - Get top management support
    - Procurement estimate was not enough as the software to purchase needed custom development. Erica got approval for additional funds from Joe, project sponsor, under the condition that the project still had to pay for itself in one year as planned
    - Survey of tools and templates had low response rate. Joe helped by sending email to all JWD's consultants and offering extra vacation days to the person who provided the best example of use

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Monitoring and Controlling

- Involves measuring progress toward project objectives, monitoring deviation from the plan, and taking correction actions
  - Occurs during all phases of the project life cycle, affects all other process groups, and involves all knowledge areas
  - Outputs include progress reports, change requests, and updates to various plans
  - See attachment document
- Weekly progress report
  - Every Friday, team members submitted what they did, what was going well, what was not and why
  - See attachment document
- Weekly timesheet
  - Every Friday by 4 pm, team members submitted actual hours of work
  - Erica and Jessie considered critical path and earned value data





Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Closing (1 of 2)

- Involves gaining stakeholder and customer acceptance of the final products and services
  - Even if projects are not completed, they should be closed out to learn from the past

TABLE 3-15 Closing processes and output

Knowledge Area	Closing Process	Outputs
Project Integration Management	Close project or phase	Project documents updates Final product, service, or result transition Final report Organizational process assets updates

Source: *PMBOK® Guide – Sixth Edition*, 2017.

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Closing (2 of 2)





- Deliver final product, service, or result
- Plan and execute transition to normal operation
- Update organizational process assets, i.e. project files
- Close out all procurement contracts
- Prepare lessons-learned report
  - Erica had her team prepare confidential individual lessons-learned report
  - Erica prepared a summary lessons-learned report
  - See attachment document
- Prepare final report, final presentation
  - See attachment document
- Have project sponsor sign a client acceptance form
- Organize project closure with team, e.g. meal, after final presentation



Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

How do process groups map onto predictive development life cycle?



Waterfall (linear process flow)

Communication	Planning	Modeling	Construction	Deployment

Process groups

Initiating	Planning	Executing	Monitoring and controlling	Closing

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Case Study 2: JWD Consulting's Project Management Intranet Site (Adaptive or Agile Approach)

- An agile project team typically uses several iterations or deliveries of software instead of waiting until the end of the project to provide one product
- Use agile when projects have
  - Less rigid constraints
  - Experienced and preferably co-located team
  - Smaller risks
  - Unclear requirements
  - More flexible scheduling
- (Use predictive when projects have
  - Heavy constraints
  - Inexperienced and disperse teams
  - Large risks
  - Clear up-front requirements
  - Fairly rigid completion date)

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Scrum Roles, Artifacts, and Ceremonies (1 of 4)

- Scrum roles
  - Product owner
    - person responsible for the business value of the project and for deciding what work to do and in what order, as documented in the product backlog
  - ScrumMaster
    - person who ensures that the team is productive, facilitates the daily Scrum, enables close cooperation across all roles and functions, and removes barriers that prevent the team from being effective
    - authority over process but not the people on the team
  - Developer
    - cross-functional team who organize themselves and the work to produce the desired results for each sprint, which normally lasts 2-4 weeks
  - All roles form a Scrum team of 10 or fewer people

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Scrum Roles, Artifacts, and Ceremonies (2 of 4)

- An artifact is a work product of the process
- Scrum artifacts
  - Product backlog
    - list of features prioritized by business value
  - Sprint backlog
    - highest-priority items from the product backlog to be completed within a sprint
  - Burndown/Burnup chart
    - shows the cumulative work remaining/done in a sprint on a day-by-day basis


Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Scrum Roles, Artifacts, and Ceremonies (3 of 4)

- Scrum ceremonies
  - Sprint planning session
    - meeting with the team to select a set of work from the product backlog to deliver during a sprint
    - Maximum eight hours; two hours for each week of sprint length
  - Daily Scrum
    - short meeting for the development team to share progress and challenges and plan work for the day
    - 15 minutes or less
  - Sprint reviews
    - meeting in which the team demonstrates to the product owner what it has completed during the sprint
    - Maximum four hours; one hour for each week of sprint length
  - Sprint retrospectives
    - meeting in which the team looks for ways to improve the product and the process based on a review of the actual performance of the development team
    - Maximum three hours; 45 minutes for each week of sprint length

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

How do process groups map onto Scrum?

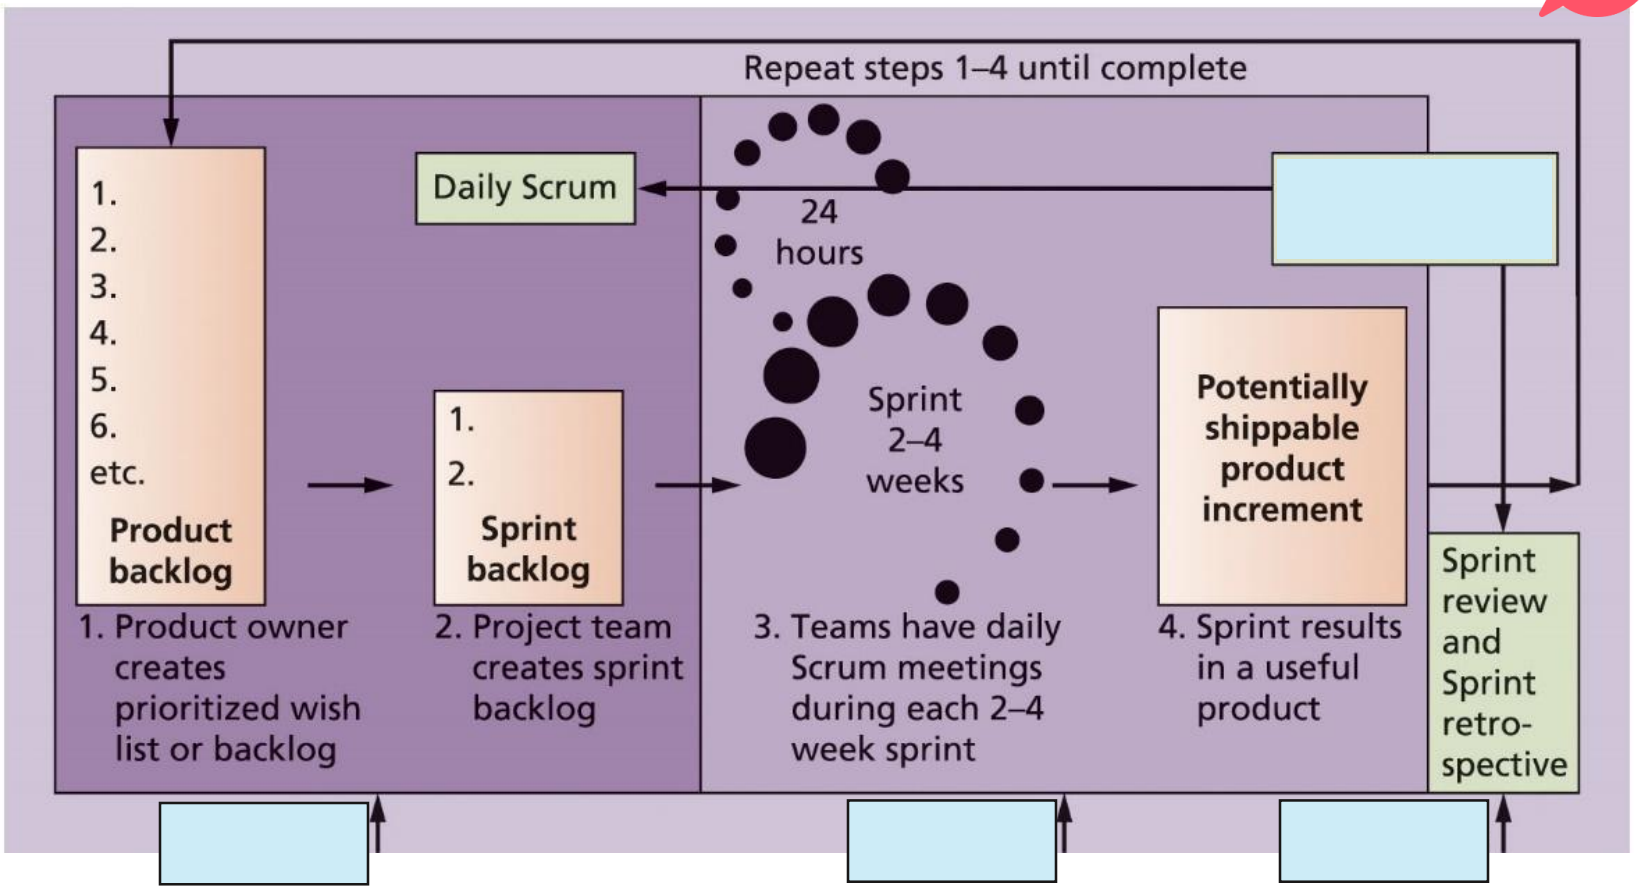

Process groups	Initiating	Planning	Executing	Monitoring and controlling	Closing

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Scrum Roles, Artifacts, and Ceremonies (4 of 4)

Process Group	Scrum Activity
Initiating	Determine roles
	Decide how many sprints will compose each release and the scope of software to deliver
Planning	Create product backlog
	Create sprint backlog
	Create release backlog
	Plan work each day in the daily Scrum
	Document stumbling blocks in a list
Executing	Complete tasks each day during sprints
	Produce a shippable product at the end of each sprint
Monitoring and controlling	Resolve issues and blockers
	Create and update burndown chart
	Demonstrate the completed product during the sprint review meeting
Closing	Reflect on how to improve the product and process during the sprint retrospective meeting

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Table 3-18 Unique Scrum activities by process group

Project Pre-Initiation and Initiation

- Main differences between pre-initiation in this case and the first case
  - Determining roles and deciding what functionality would be delivered as part of each release
  - How many sprints will be required to complete a release
  - How many releases of software to deliver
- Business case, project charter, stakeholder register, stakeholder management strategy, kick-off meeting would still be created
- Roles
  - Product owner: Joe
  - ScrumMaster: Erica
  - Developer: other people
- 4-week sprint, 3 releases given time and cost constraints
- UI prototype could be useful for users to get the look and feel and give feedback





Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (1 of 3)

- Because Scrum implies that team members work as a self-directed group, coached by the ScrumMaster, a team charter should not be necessary
- Descriptions of work are identified in the product backlog and sprint backlog, rather than WBS
- More detailed work is documented in user stories and associated tasks
- Team must estimate a velocity (or capacity) for each sprint based on team member availability each day
  - Estimates can be provided as hours of work or story points

Story points	Story
1	• As a player, I want a new hairstyle for the main character. (Base story) • As a player, I want the attack power of Monkey-king to be decreased
2	• As a player, I want a new Christmas season makeover for all heroes • As a player, I want a new Halloween season makeover for all villains
3	• As a player, I want a new special quest in the game

T-shirt Size	Story Points	Duration
XS	1	Minutes - 1,2 Hours
S	2	Half a day
M	3	1-2 days
L	5	Half week
XL	8	Week
XXL	13	More than 1 week
XXL	21	Full Sprint

l, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

https://clickup.com/blog/agile-story-points/
https://rubygarage.org/blog/3-reasons-to-estimate-with-story-points
https://medium.com/@syalindania/agile-story-points-in-scrum-faff6e175ad5

Member portal of Healthcare solution	
Claims→ Theme	
Manage Claims → Epic	
User Story 1 As a member I want to view my current unpaid claims so that I can keep track of them. **Acceptance criteria** • Verify that only pending claims are listed. • Verify that claims are listed by dates • Verify that all claims of dependent are listed	**User Story 2** As a member I want to view the details of a claim so that I have the clarity. **Acceptance criteria** • Verify that all details related to claims are listed i.e. Member name, claim amount, claim purpose etc. • Verify that all the related approvals and files are attached in the claims details
Tasks: Create UI screen for showing the results Write business logic to get the value from DB Review Test cases Validate the result	**Tasks:** Create a DB table to populate the data Create UI screen to show the claim data Write logic to export data from 3rd party sys



ngage. May not be copied, scanned, or duplicated, in whole or in part, except
ice or otherwise on a password-protected website for classroom use.

Project Planning (2 of 3)

Several process groups are repeated for each sprint, resulting in several releases (3)

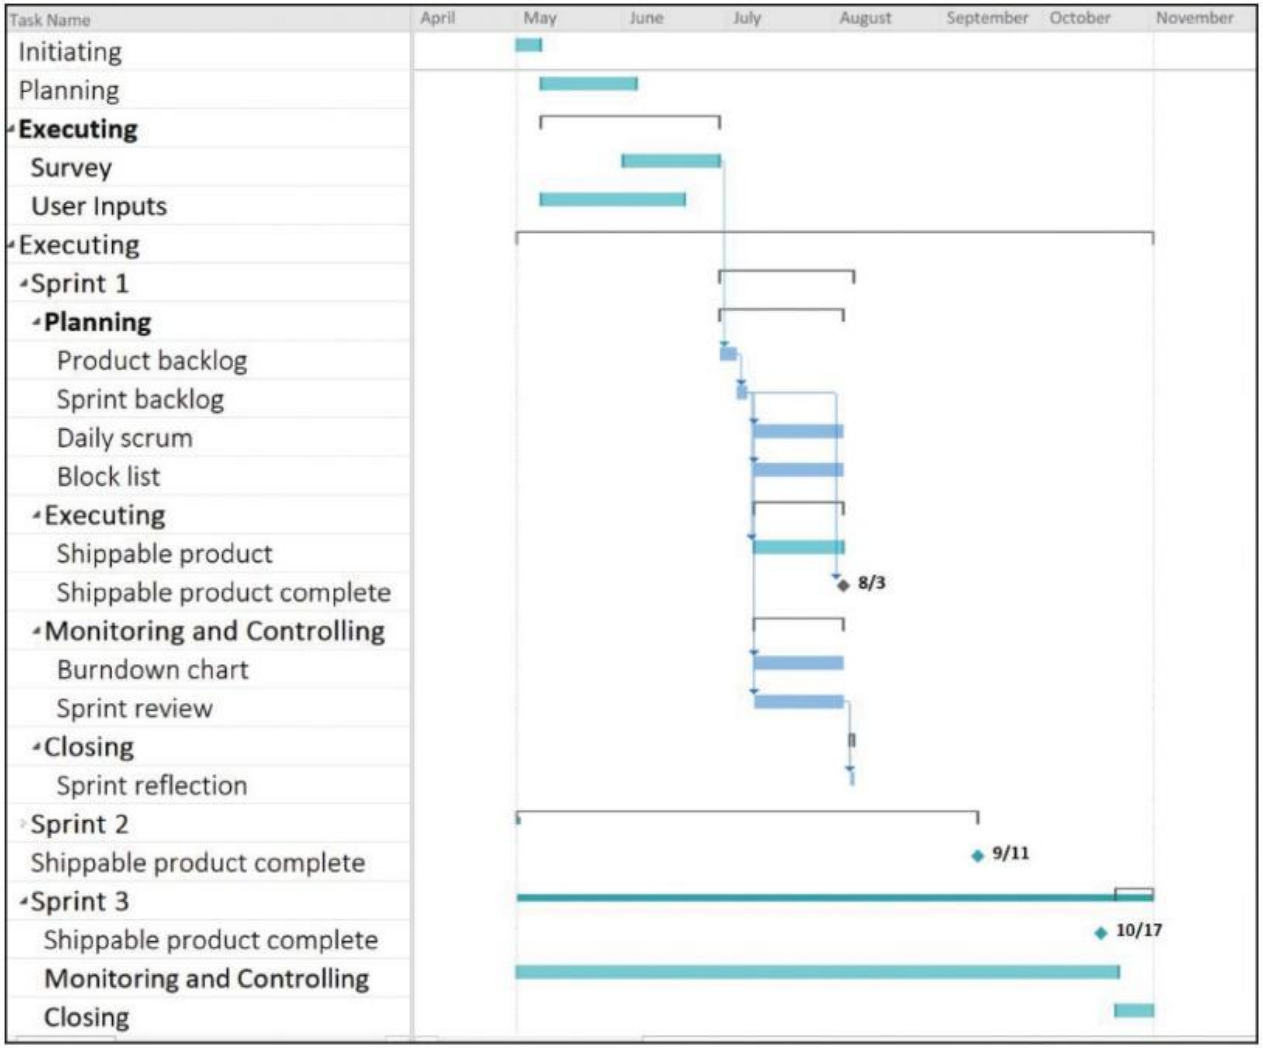








FIGURE 3-6 Intranet site project baseline Gantt chart using Scrum approach

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Planning (3 of 3)

Scrum team breaks down sprint backlog items into user stories and then tasks, similar to tasks in WBS







Product Backlog	Sprint Backlog
1. User story templates, samples, and point person	1. User story templates, samples, and point person
2. WBS templates, samples, and point person	2. WBS templates, samples, and point person
3. Project schedule templates, samples, and point person	3. Project schedule templates, samples, and point person
4. Ability to charge customers for some intranet products and services	4. Ability to charge customers for some intranet products and services
5. Ability to collect user suggestions	5. Ability to collect user suggestions
6. Business case templates, samples, and point person	
7. Ask the Expert feature	
8. Stakeholder management strategy templates, samples, and point person	
9. Risk register templates, samples, and point person	
10. Etc.	

Table 3-19 Product and Sprint Backlogs


Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Execution

- The most time and money should be spent on executing
  - Plans are implemented to create the desired product
- Agile approach: team produces several iterations of a potentially shippable product
  - Users can access and make suggestions
- Communications are different
  - Project team meets every morning, physically or virtually








Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Monitoring and Controlling (1 of 5)

- The two main tools for monitoring and controlling in the Scrum framework
  - Daily Scrum: held each morning to plan and communicate work for the day and discuss any risks, issues, or blockers which the ScrumMaster has to handle
  - Sprint review: work progress within a sprint can be represented on a sprint board maintained by the ScrumMaster
    - Sprint review demonstration to the product owner to show what has been completed during the sprint
    - Burndown chart: an important artifact used to graphically display progress on each sprint, plotting each day's sum of hours or story points remaining

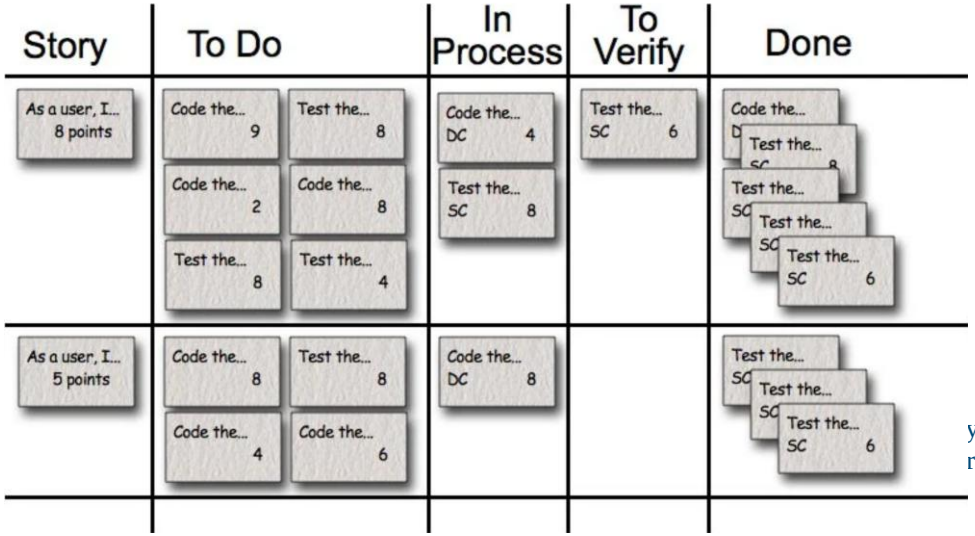




y not be copied, scanned, or duplicated, in whole or in part, except rwise on a password-protected website for classroom use.

https://www.mountaingoatsoftware.com/agile/scrum/scrum-tools/task-boards

Project Monitoring and Controlling (2 of 5)

Traditional sprint board

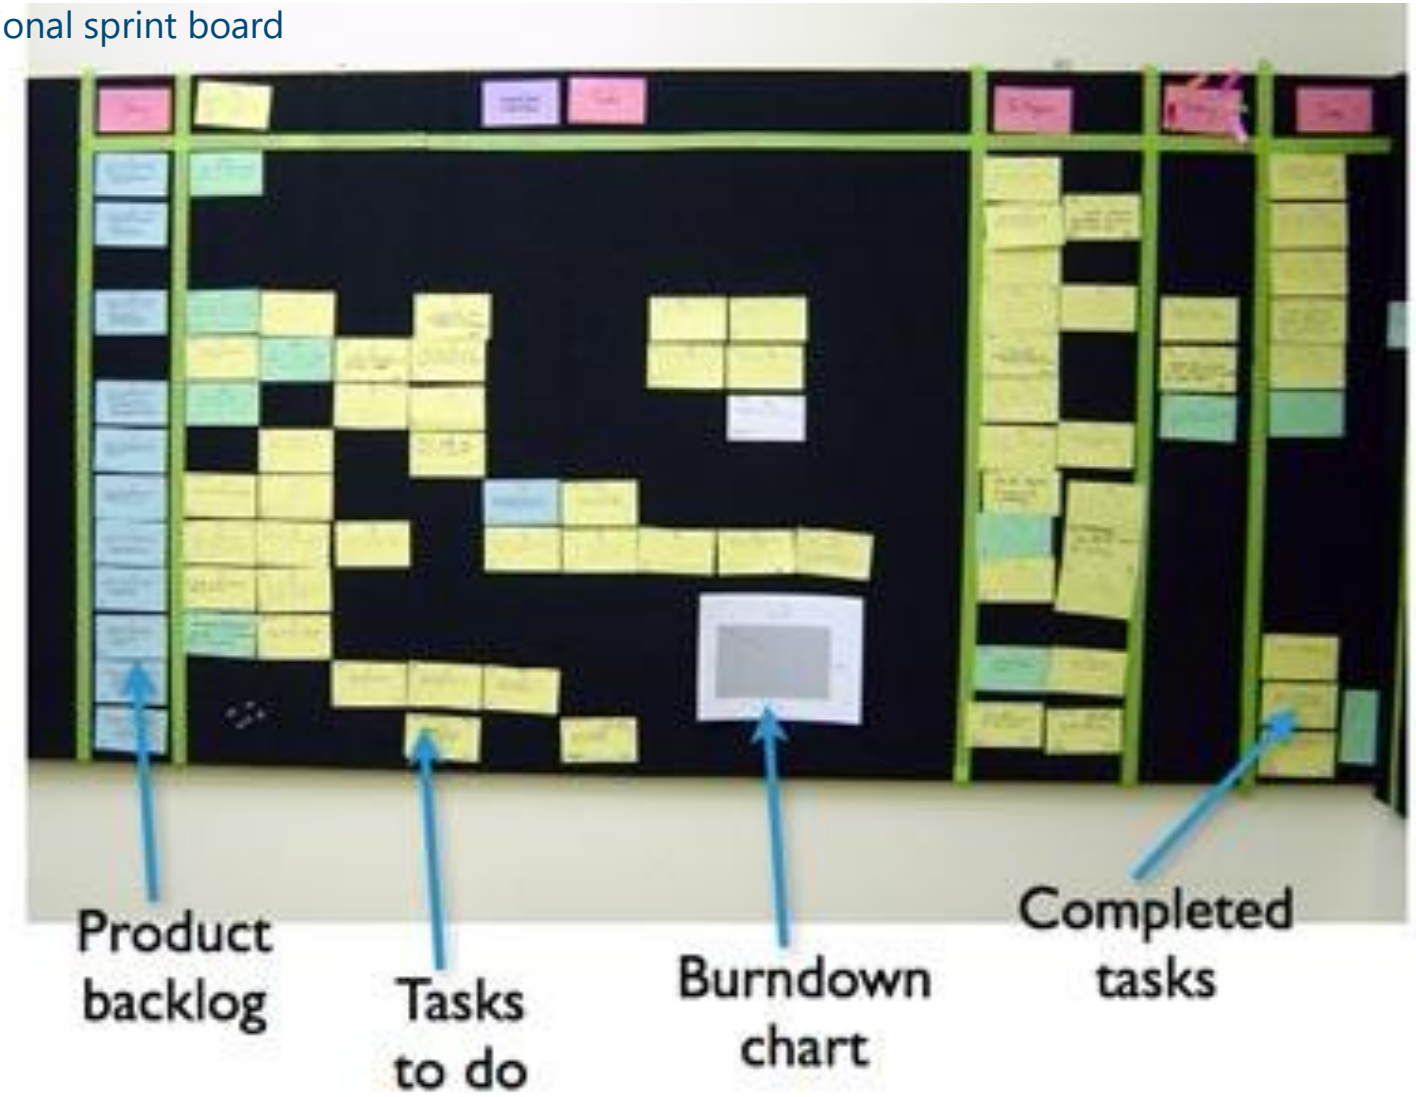


Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

https://www.mountaingoatsoftware.com/agile/scrum/scrum-tools/task-boards

Project Monitoring and Controlling (3 of 5)

Modern sprint board

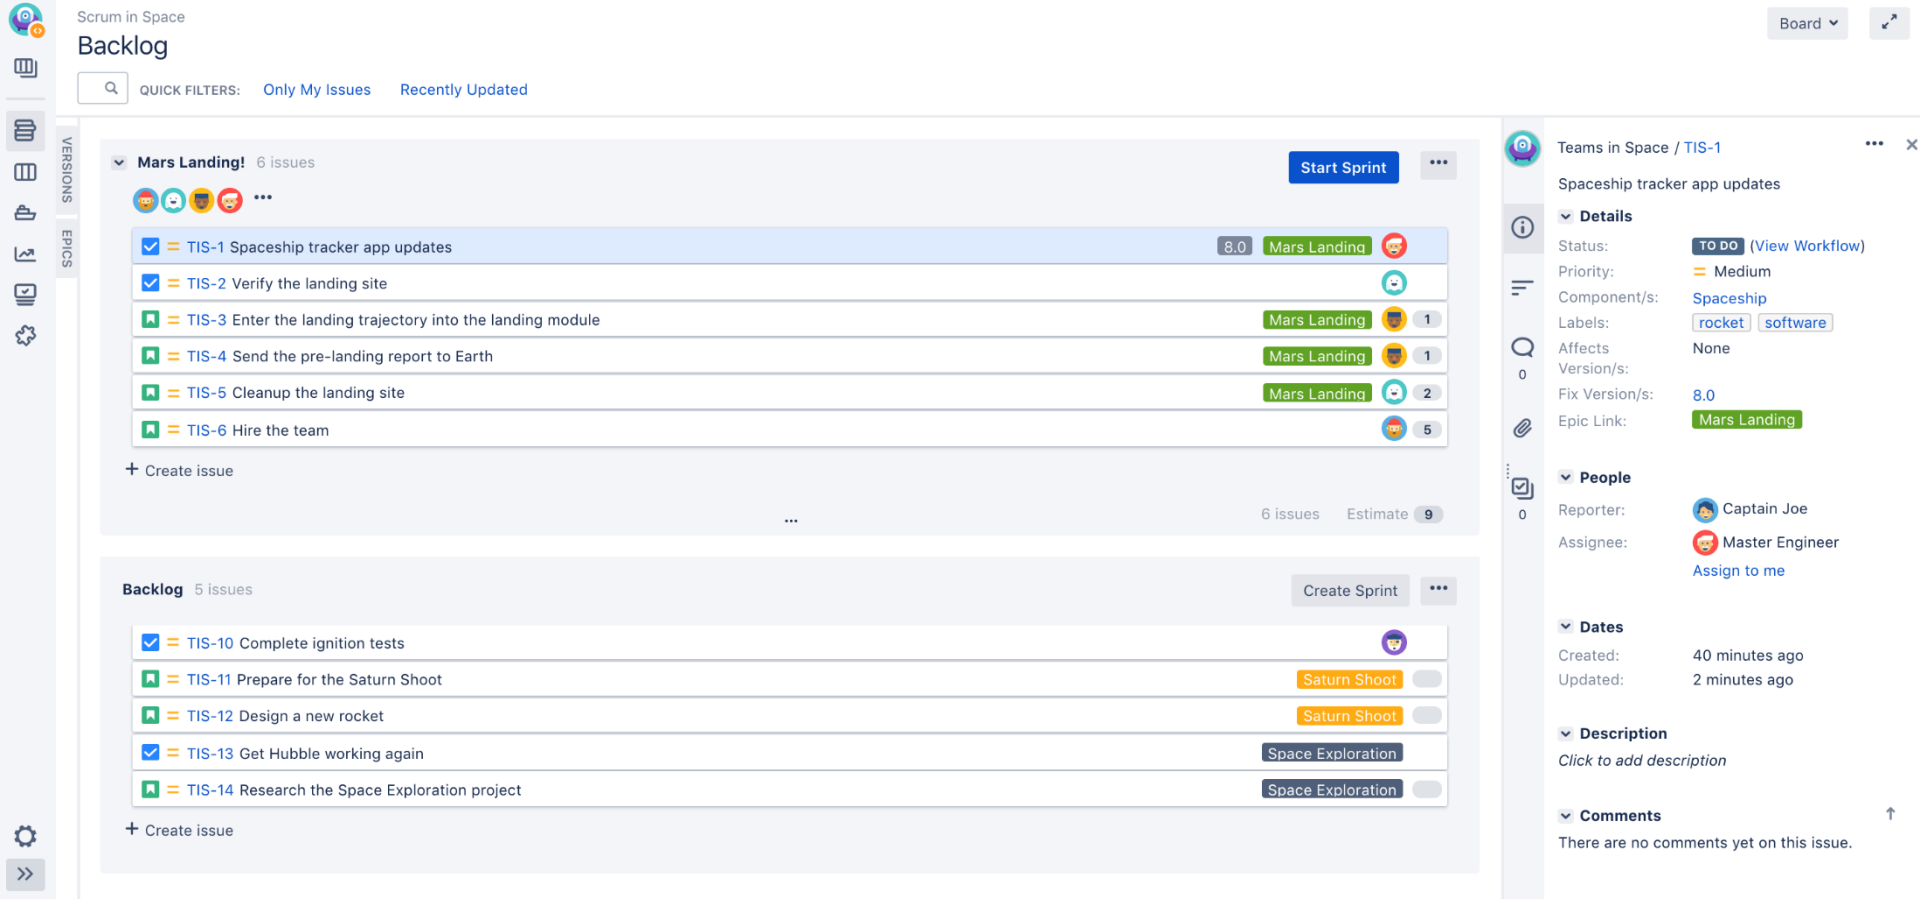


Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

https://confluence.atlassian.com/jirasoftwareserver/using-your-scrum-backlog-938845361.html

Project Monitoring and Controlling (4 of 5)

Modern sprint board

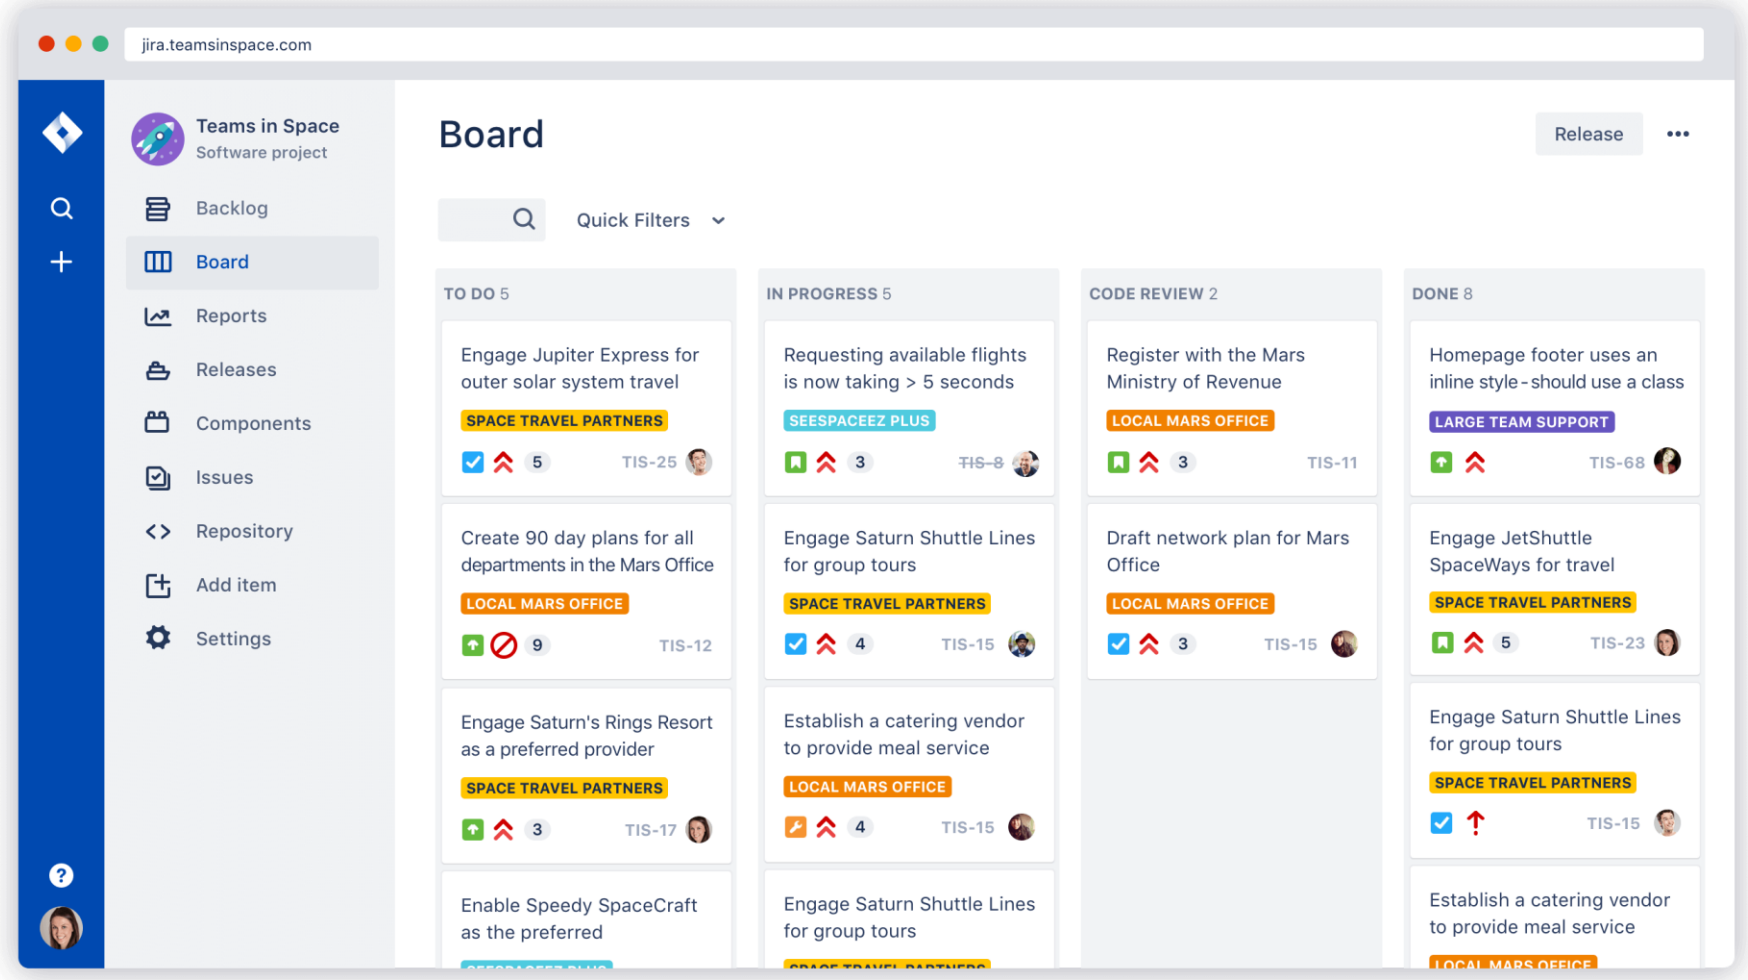

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

https://www.atlassian.com/software/dev-tools

Project Monitoring and Controlling (5 of 5)

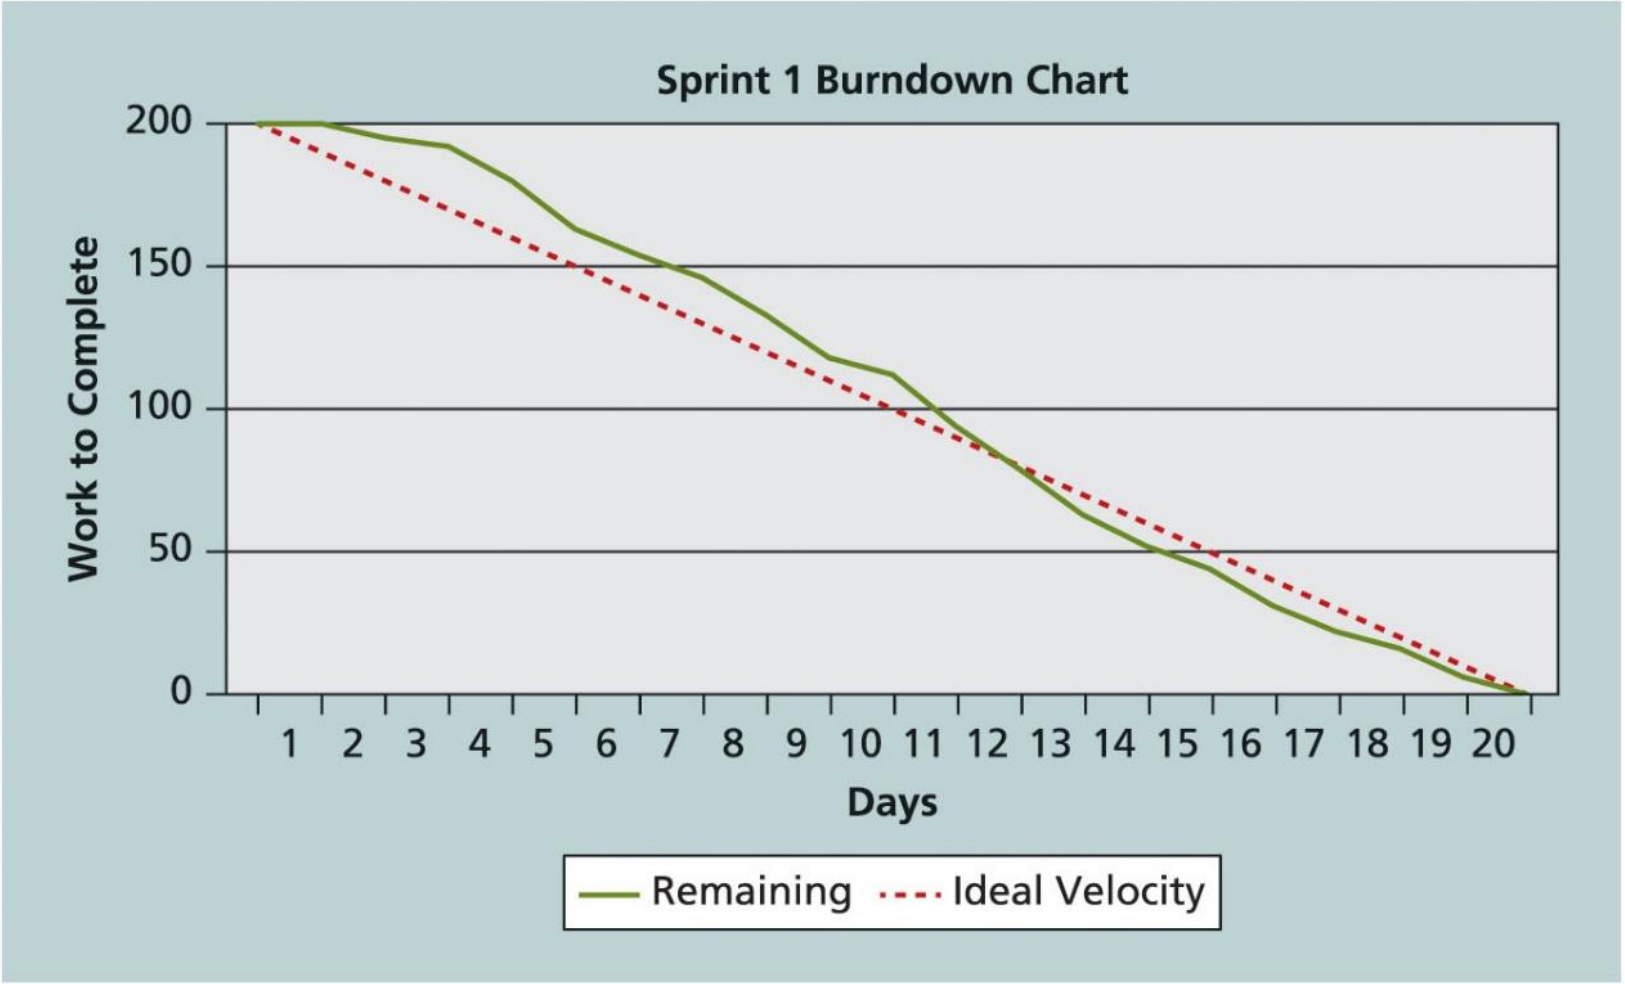


FIGURE 3-7 Burndown chart

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Project Closing



- After the sprint review, the ScrumMaster leads a sprint retrospective
  - Team reflects on what happened during the sprint, similar to a lessons-learned report but on a shorter period of time
- Sprint retrospective is intended to answer two fundamental questions
  - What went well during the last sprint that we should continue doing?
  - What could we do differently to improve the product or process?
- Suggested action items for implementation could be added to the product backlog if agreed by the product owner

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Templates by Process Group

- See attachment document 

Karate Kid concepts of project management https://www.youtube.com/watch?v=Msn6YHZPKyw

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.

Chapter Summary

- The five project management process groups are initiating, planning, executing, monitoring and controlling, and closing
- You can map the main activities of each process group to the ten knowledge areas
- The JWD Consulting case study provides an example of using the process groups and shows several important project documents
- The second version of the same case study illustrates how to use Scrum, the leading agile method, to manage the project

Information Technology Project Management, Ninth Edition. © 2019 Cengage. May not be copied, scanned, or duplicated, in whole or in part, except for use as permitted in a license distributed with a certain product or service or otherwise on a password-protected website for classroom use.
