CHULALONGKORN UNIVERSITY · FACULTY OF ENGINEERING

Seating & Event Availability Tracking System (SEATS) for La Loy Restaurant

Milestone 2 Final Deliverable:
Project Management Plan — Scope, WBS, Effort, Resources, Cost Baseline, Gantt Chart and Critical Path

Course: 2110722 Software Project Management
Submitted to: Assoc. Prof. Twittie Senivongse

By: SE69 Group 1 (regular program)
• Boonnisa Tangjitpermkwamdee Student ID 6970156821
• Sirapatr Chalermwattanatrai Student ID 6970292421
• Chawanakorn Sanannam Student ID 6970064721
• Watayut Aiamanan Student ID 6970267821

Version 1.0 · October 2026
Department of Computer Engineering, Faculty of Engineering, Chulalongkorn University
Semester 1, Academic Year 2569

Table of Contents

1. Project Scope Statement....3
1.1. Project summary....3
1.2. Product characteristics and requirements....3
1.3. Project deliverables....3
1.4. Exclusions....4
1.5. Success criteria....4
2. Work Breakdown Structure (WBS) and Tasks....4
2.1. WBS dictionary (summary)....6
2.2. WBS dictionary (worked examples)....6
3. Effort Estimation....6
3.1. Effort by role....7
4. Human and Physical Resource Assignment and Rates....7
5. Cost Estimate....8
5.1. Cost-control rules....8
6. Schedule, Gantt Chart and Critical Path....8
6.1. Iteration schedule....9
6.2. Gantt chart view....9
6.3. Critical path (dependency-based planning estimate)....10
6.4. Milestone control points....10
7. Conclusion....11

1. Project Scope Statement

1.1. Project summary

The Seating & Event Availability Tracking System (SEATS) is a LINE-integrated web application for reserving tables at La Loy Restaurant's live-music concerts. Customers use a LIFF web app to browse concerts, view a live table map, select a table, hold it for 15 minutes, pay the full table fee through a payment gateway, and receive a QR e-ticket. Restaurant staff use a shared back office to monitor bookings, handle exceptions and scan QR codes at check-in. The system uses one central record to reduce double bookings and payment-related disputes. After the initial implementation, the system is piloted at La Loy and productized as a multi-tenant subscription service for other live-music restaurants.

The project runs from 3 August 2026 to 28 July 2028 (24 calendar months / 2 project years): Year 0 builds and deploys Release 1.0 Core (2 April 2027) and Release 2.0 Growth (30 July 2027); Year 1 runs the live pilot and delivers Release 2.1 SaaS productization (11 February 2028), closing with the expansion decision on 28 July 2028.

1.2. Product characteristics and requirements

The functional requirements use the R1-R7 identifiers of the requirements-engineering report; the quality and compatibility characteristics are taken from the project-management report.

Requirement / area	In-scope characteristics / requirements
R1 (LINE self-service channel)	Mobile-first LIFF web app accessed via the LINE Rich Menu to browse concert rounds, view a live table map, select packages/tables and obtain QR e-tickets.
R2 (Real-time hold and inventory control)	One central database with an automatic 15-minute table lock (first lock wins) that prevents double bookings; table status is maintained in real time.
R3 (Automated payment gateway)	Payment-gateway checkout (PromptPay QR and cards) with automatic webhook confirmation of the full table fee.
R4 (Shared back-office console)	Real-time web dashboard for Manager, Owner and Front Staff to manage rounds, table layouts, pricing packages, manual overrides and audit trails.
R5 (Door check-in and validation)	Mobile QR e-ticket scanning at the venue door, target check-in time of no more than 15 seconds per table, with instant name/phone lookup.
R6 (Growth features, Release 2.0)	Automated LINE push reminders, 30-minute grace extension, waitlist queuing, official booking transfer and operational reports.
R7 (Multi-tenant architecture, Release 2.1)	Multi-tenant data isolation, self-service venue onboarding, subscription plans and limits (Free, Standard, Premium), automated tier enforcement and administrative billing.
Quality and operations	Target response time of no more than 2 seconds for customer/front-staff transactions; check-in within 15 seconds per table; support at least 5 transactions per second at booking-open; daily backup with Excel export; recovery within 2 hours during opening hours.
Compatibility and compliance	Current LINE in-app browser and the last two versions of Chrome, Safari and Edge; consent, data-retention and correction handling designed into the system.

1.3. Project deliverables

Category	Deliverables
Project-management deliverables	Project charter and scope statement; stakeholder list and organization; Development Case; Software Development Plan; WBS and WBS dictionary; iteration plans; effort, resource, cost and schedule baselines; risk, quality and communication plans; status and iteration assessments; change-request records; milestone reviews; pilot review; hand-over and lessons-learned records.
Requirements and design	Vision; Glossary; Stakeholder Requests; Business Rules; Domain Model; Use-Case Model and specifications; Software Requirements Specification (SRS); Supplementary Specification; Analysis Model; Software Architecture Document; user-interface prototype; test plan and test cases.
Product deliverables	Release 1.0 Core in operation at La Loy by 2 April 2027; Release 2.0 Growth in operation by 30 July 2027; productized Release 2.1 by 11 February 2028; test results; training for Manager and Front Staff; current-booking data migration; operating/support hand-over.
Closure deliverables	Pilot KPI results, expansion decision record, hand-over record, lessons learned, final status assessment and sponsor/customer sign-off.

1.4. Exclusions

- Split payments among multiple customers.
- Customer-facing table photographs or distance-to-stage comparisons.
- Restaurant-configurable booking rules beyond the rules agreed for the defined releases.
- Payment-gateway fees, each restaurant's LINE Official Account plan and the pilot restaurant's own check-in tablet are not costs paid by the software house in this project budget.
- Subscription revenue after the expansion decision and expansion operations beyond the project period are outside this project delivery budget.

1.5. Success criteria

Success criterion	Target / evidence
Release milestones	Release 1.0 operating at La Loy by 2 Apr 2027; Release 2.0 by 30 Jul 2027; Release 2.1 by 11 Feb 2028; total project budget not above 1,010,590 THB.
Booking integrity	Zero double bookings on La Loy concert nights after go-live; table status maintained in real time on one record.
Customer experience	Booking completed within 3 minutes from table selection to confirmation without requiring a Manager reply.
Business outcome	No-show rate at La Loy reduced by 35% within six months of Release 2.0.
Operational quality	Check-in within 15 seconds per table; at least 5 transactions per second at booking-open; transaction response time no more than 2 seconds; recovery within 2 hours during opening hours.
Cost ceiling	Restaurant hosting, APIs and LINE plan at or below 1,000 THB/month.
Expansion gate	La Loy meets pilot criteria and continues on a paid plan; at least 10 restaurants are on the waiting list; Release 2.1 meets the per-shop hosting/support cost assumptions.

2. Work Breakdown Structure (WBS) and Tasks

The WBS is presented in a detailed schedule format, following the required headings: WBS ID, task, responsible role, duration, predecessor(s), start, finish, and expected output/milestone measure. Iteration dates follow the SEATS report; task-level durations and dependencies are planning estimates. The phase rows (0, 1, 2, 3, 4, 5, 6, 7, 8) are shown as navy bands.

WBS ID	Task	Responsible Role	Duration	Predecessor(s)	Start	Finish	Expected Output / Milestone Measure
0	Project initiation and risk-driven planning	Project Manager + Team	4d	Start	3 Aug 2026	6 Aug 2026	Project kickoff; initial scope and stakeholder access confirmed
0.1	Confirm project objectives, stakeholders, and initial risks	Project Manager + System Analyst	2d	Start	3 Aug 2026	4 Aug 2026	Stakeholder list and initial risk list
0.2	Define high-level scope, assumptions, and constraints	Project Manager + System Analyst	2d	0.1	5 Aug 2026	6 Aug 2026	Initial scope baseline
1	Inception — planning and LCO	Project Manager + Team	23d	0	3 Aug 2026	2 Sep 2026	LCO milestone approved
1.1	Elicit business problem and high-level features (I1)	System Analyst + Requirements Specifier	16d	0.2	3 Aug 2026	24 Aug 2026	Problem statement, stakeholders, high-level features
1.2	Prepare Vision, Business Case, Development Case and WBS (I2)	Project Manager + System Analyst	7d	1.1	25 Aug 2026	2 Sep 2026	Plans and WBS ready; LCO on 2 Sep 2026
2	Elaboration — requirements and architecture	System Analyst + Team	37d	1	3 Sep 2026	23 Oct 2026	LCA milestone approved
2.1	Specify reservation and QR check-in use cases (E1)	System Analyst + Requirements Specifier	10d	1.2	3 Sep 2026	16 Sep 2026	Use-case specifications, SRS and Supplementary Specification
2.2	Create analysis model, architecture, UI prototype and test plan (E2)	System Analyst + Designer + QA	27d	2.1	17 Sep 2026	23 Oct 2026	Architecture and SRS baseline; LCA on 23 Oct 2026
3	Release 1.0 Core — construction	Requirements Specifier/Designer + System Analyst + QA	84d	2	26 Oct 2026	26 Feb 2027	Core build reaches IOC
3.1	Build concert setup, zones, packages, table map and 15-minute hold (C1)	Designer + System Analyst	40d	2.2	26 Oct 2026	18 Dec 2026	Table selection and hold workflow
3.2	Implement payment gateway, callbacks and staff accounts (C1)	System Analyst + Designer	40d	2.2	26 Oct 2026	18 Dec 2026	Payment and staff access functions

WBS ID	Task	Responsible Role	Duration	Predecessor(s)	Start	Finish	Expected Output / Milestone Measure
3.3	Implement QR e-ticket, check-in, live booking view, audit and backup (C2)	Designer + System Analyst + QA	40d	3.1, 3.2	4 Jan 2027	26 Feb 2027	Core functions integrated; IOC on 26 Feb 2027
4	Release 1.0 — transition and go-live	QA + Project Manager + Restaurant users	25d	3	1 Mar 2027	2 Apr 2027	Release 1.0 in operation
4.1	Run acceptance/load tests, train staff and migrate current bookings (T1)	QA + Project Manager + Manager	25d	3.3	1 Mar 2027	2 Apr 2027	Go-live at La Loy by 2 Apr 2027
5	Release 2.0 Growth	Whole project team	84d	4	5 Apr 2027	30 Jul 2027	Release 2.0 in operation
5.1	Implement reminders, grace extension, waitlist, transfers and reports (C3)	Designer + System Analyst + Requirements Specifier	60d	4.1	5 Apr 2027	25 Jun 2027	Growth features integrated
5.2	Test, train users and deploy Release 2.0 (T2)	QA + Project Manager + Restaurant users	25d	5.1	28 Jun 2027	30 Jul 2027	Release 2.0 live by 30 Jul 2027
6	Pilot operation and KPI monitoring (P1)	Project Manager + QA + Restaurant Manager	261d	5.2	2 Aug 2027	28 Jul 2028	Pilot KPIs recorded on concert nights
6.1	Measure booking time, double bookings, no-shows, check-in and operating cost	Project Manager + QA + Manager	During pilot	5.2	2 Aug 2027	28 Jul 2028	Evidence for expansion gate
7	Release 2.1 productization	System Analyst + Designer + QA	120d	5.2	2 Aug 2027	11 Feb 2028	Multi-tenant subscription product ready
7.1	Implement multi-tenant model, plans/limits, billing and self-service onboarding (C4)	System Analyst + Designer + Requirements Specifier	120d	5.2	2 Aug 2027	14 Jan 2028	Release 2.1 productization build
7.2	Test and deploy Release 2.1 (T3)	QA + Whole project team	20d	7.1	17 Jan 2028	11 Feb 2028	Release 2.1 by 11 Feb 2028
8	Project closure and expansion decision	Project Manager + Sponsor + Restaurant Owner	5d	6.1, 7.2	24 Jul 2028	28 Jul 2028	Pilot review, hand-over, lessons learned and expansion decision

2.1. WBS dictionary (summary)

Each work package must have exactly one accountable owner role, defined acceptance evidence and a reviewer who is not the author. The Project Manager maintains the WBS baseline and records approved changes through the Change Control Board. Construction includes implementation by the Requirements Specifier/Designer and independent verification by the QA role, as described in the SEATS report.

2.2. WBS dictionary (worked examples)

Two architecturally critical work packages are expanded as full WBS dictionary entries with measurable acceptance criteria and precedence. The entries are contributed by the Requirements Specifier (Chawanakorn Sanannam) and are mapped to the WBS identifiers of Section 2.

Field	3.1 Table selection, hold and inventory rules	3.3 QR e-ticket and check-in
Accountable owner	System Analyst / Designer	Designer
Inputs	Use-case specifications; table/zone/package data model.	Confirmed booking record; payment-gateway confirmation webhook.
Outputs	Table map, 15-minute hold logic and inventory rules.	Signed QR e-ticket and door-validation endpoint.
Acceptance criteria	An automated test of 50 concurrent requests for the same table yields exactly 1 successful hold and 49 conflict rejections without deadlock; the hold releases at 15 minutes ± 5 seconds.	A unique signed QR code is generated per confirmed booking; tampered references are rejected; the validation endpoint responds in < 2 seconds; duplicate scans raise a warning to Front Staff.
Predecessor	2.2 (requirements and architecture baseline)	3.1 (hold) and 3.2 (payment)

3. Effort Estimation

The source report's top-down baseline is 2,632 person-hours: 2,092 hours in Year 0 for the build and 540 hours in Year 1 for productization. The task-level split below is an indicative bottom-up planning estimate created for this deliverable; the totals reconcile exactly to the source baseline (0% percent difference) and to the labor cost of 846,600 THB.

WBS ID	Work package group	Estimated effort (hours)	Period
0–1.2	Initiation, planning and LCO	128	Year 0
2.1–2.2	Requirements, analysis, architecture and prototype	320	Year 0
3.1–3.3	Release 1.0 construction	800	Year 0
4.1	Release 1.0 testing, training and go-live	190	Year 0
5.1	Release 2.0 construction	504	Year 0
5.2	Release 2.0 test and deployment	150	Year 0
6 + 7.1	Pilot monitoring and Release 2.1 construction	480	Year 1
7.2 + 8	Release 2.1 testing and close-out	60	Year 1
TOTAL		**2,632**	**Year 0: 2,092; Year 1: 540**

3.1. Effort by role

Role / team member	Hours	Rate (THB/hour)	Labor cost (THB)
Project Manager / Change Control Manager — Boonnisa Tangjitpermkwamdee	434	350	151,900
System Analyst / Software Architect — Sirapatr Chalermwattanatrai	706	350	247,100
Requirements Specifier / UI Designer / Designer — Chawanakorn Sanannam	842	300	252,600
Quality Assurance / Tester — Watayut Aiamanan	650	300	195,000
TOTAL	**2,632**	**—**	**846,600**

The four engineers are part-time resources. The report assumes approximately 6–16 hours per week per engineer in Year 0 and 2–7.5 hours per week per engineer in Year 1, alongside other software-house work. This keeps every resource at or below 100% utilization; the Year-1 SaaS work (C4, T3) is deliberately back-loaded into the post-pilot window to remove the peak that would otherwise fall on the System Analyst and the Requirements Specifier.

4. Human and Physical Resource Assignment and Rates

Table below maps each human and physical resource to its assignment / responsibility and its rate or cost basis. Human rates are internal cost rates for 2026, expressed per hour and identical to the Milestone 1 rate baseline (350 THB/h for the PM/CM and SA roles; 300 THB/h for the RS/Designer and QA roles).

Resource	Assignment / responsibility	Rate or cost basis
Boonnisa Tangjitpermkwamdee	Project Manager and Change Control Manager; plans and controls scope, schedule, budget and risks; owns plans, iteration assessments, change control and closure.	350 THB/hour; 434 hours; 151,900 THB
Sirapatr Chalermwattanatrai	System Analyst and Software Architect; leads elicitation, use-case model, architecture, integration assessment and technical design.	350 THB/hour; 706 hours; 247,100 THB
Chawanakorn Sanannam	Requirements Specifier, User-Interface Designer and Designer; specifies requirements, prototypes the UI and contributes to implementation.	300 THB/hour; 842 hours; 252,600 THB
Watayut Aiamanan	Quality Assurance / Tester; test planning, independent review, functional, regression, load and acceptance testing.	300 THB/hour; 650 hours; 195,000 THB
Android phone and 10-inch tablet	Test devices for LINE in-app browser and check-in workflow; software-house project equipment.	One set; 15,000 THB
Cloud hosting, domain and development services	Development, staging and pilot hosting and domain.	Year 0 total 8,300 THB
Company/legal setup and pilot support	Registration/legal documents plus pilot hosting and support.	Year 1 total 52,200 THB (15,000 setup/legal; 37,200 hosting/support)
Pilot restaurant check-in tablet	Purchased by La Loy, not by the software house.	Excluded from project-house CAPEX; about 9,000 THB (restaurant)

External dependencies include the LINE Platform / LIFF / Messaging API and the payment gateway. The restaurant maintains its own merchant account and LINE plan; gateway fees and the restaurant's LINE plan are not included as software-house costs.

5. Cost Estimate

The cost baseline below follows the SEATS report. Labor costs are consistent with the role hours and internal rates (Table 3.1). Following the PMBOK budget build-up, the activity/work-package estimates plus the contingency reserve form the cost baseline, and the cost baseline plus any management reserve forms the project budget.

Cost item	Basis	Year 0 (THB)	Year 1 (THB)	Total (THB)
Development labor	2,092 h in Year 0; 540 h in Year 1	674,600	172,000	846,600
Test devices (CAPEX)	Android phone and 10-inch tablet	15,000	0	15,000
Hosting and services / domain	Development, staging and pilot hosting	8,300	—	8,300
Company/legal setup, pilot hosting and support	Year 1 registration, legal, hosting and support	0	52,200	52,200
Contingency reserve	10% reserve as stated in the source report	69,790	18,700	88,490
TOTAL PROJECT BUDGET		**767,690**	**242,900**	**1,010,590**
Less: La Loy pilot implementation fee	Revenue within the project	(150,000)	0	(150,000)
NET SOFTWARE-HOUSE INVESTMENT				**860,590**

5.1. Cost-control rules

- The Project Manager tracks actual effort against the 2,632-hour plan and the labor-cost baseline at each iteration assessment.
- Any change affecting scope, budget or milestone dates must be assessed for impact and decided by the Change Control Board.
- The contingency reserve is held for identified project risks; it is not treated as planned feature-development effort.
- The budget excludes costs that the source report assigns to the restaurant, including its own LINE plan, merchant-account gateway fees and check-in tablet.
- The source report describes the estimate as top-down and says a bottom-up WBS estimate should replace it at Milestone 2; the task-level breakdown in this document is therefore provisional until reviewed.

6. Schedule, Gantt Chart and Critical Path

The schedule follows the tailored Rational Unified Process (RUP) iterations in the SEATS report. The dates and milestone targets below are source-derived; the dependency chain and critical-path interpretation are planning analysis based on the listed work.

6.1. Iteration schedule

Iteration / activity	Start	Finish	Main activity / milestone	Predecessor (planning)
I1 — Inception	3 Aug 2026	24 Aug 2026	Scope, stakeholders, initial elicitation	—
I2 — Inception	25 Aug 2026	2 Sep 2026	Vision, plans, WBS; LCO	I1

Iteration / activity	Start	Finish	Main activity / milestone	Predecessor (planning)
E1 — Elaboration	3 Sep 2026	16 Sep 2026	Use cases, SRS, supplementary requirements	I2
E2 — Elaboration	17 Sep 2026	23 Oct 2026	Architecture, analysis, prototype, test plan; LCA	E1
C1 — Construction	26 Oct 2026	18 Dec 2026	Concert setup, table map/hold, payment, staff accounts	E2
C2 — Construction	4 Jan 2027	26 Feb 2027	QR, check-in, live view, audit, backup; IOC	C1
T1 — Transition	1 Mar 2027	2 Apr 2027	Pilot, training, migration; Release 1.0	C2
C3 — Construction	5 Apr 2027	25 Jun 2027	Release 2.0 Growth features	T1
T2 — Transition	28 Jun 2027	30 Jul 2027	Testing/training; Release 2.0	C3
P1 — Pilot	2 Aug 2027	28 Jul 2028	Pilot KPI measurement on concert nights	T2
C4 — Construction	2 Aug 2027	14 Jan 2028	Multi-tenant productization, plans, billing	T2; runs during P1
T3 — Transition	17 Jan 2028	11 Feb 2028	Release 2.1 testing/deployment	C4
Close-out	24 Jul 2028	28 Jul 2028	Pilot review, expansion decision, hand-over	P1 and T3

6.2. Gantt chart view

Figure 1 presents the Gantt chart of the schedule baseline across the full 24-month project window (August 2026 – July 2028). The chart shows the iteration bars for each RUP phase together with the phase-gate milestones: LCO, LCA, IOC, the Release 1.0 and Release 2.0 go-lives, the Release 2.1 SaaS launch and project close-out.

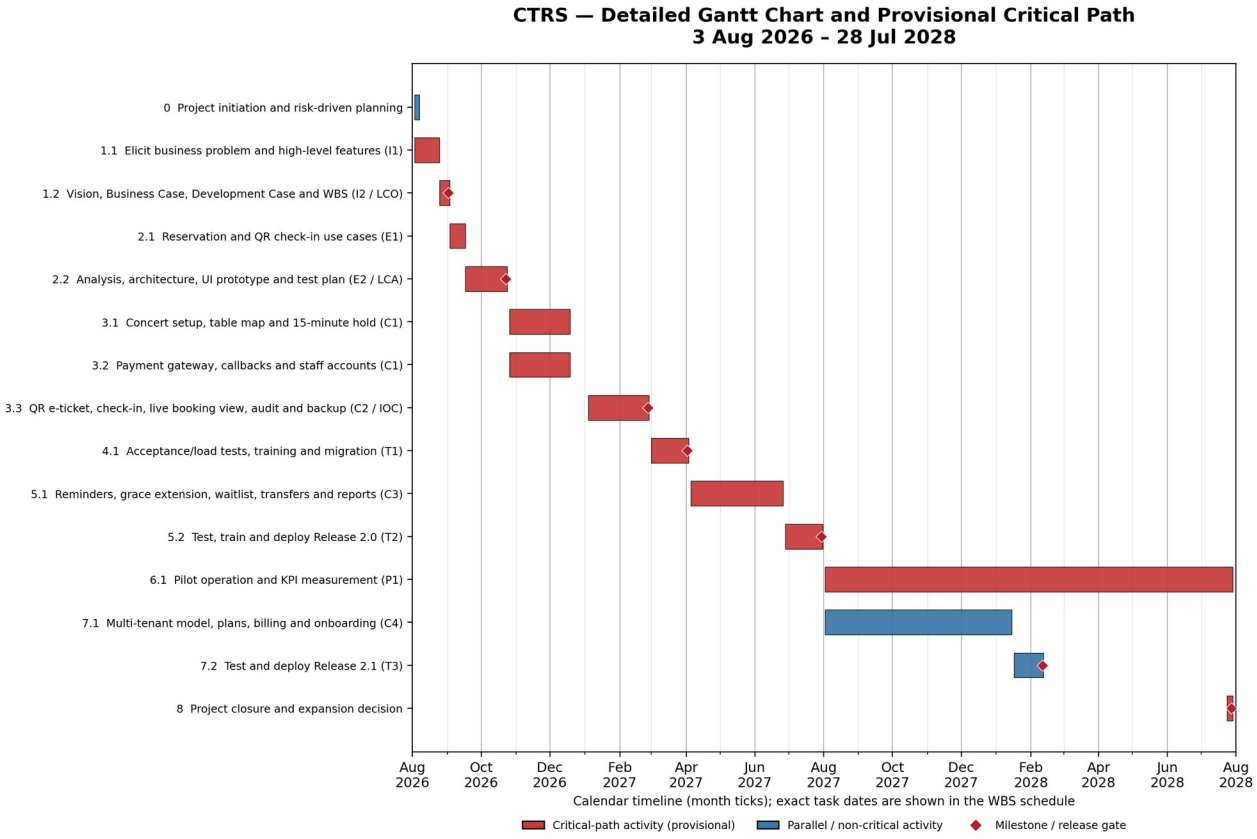


Figure 1. Gantt chart of the SEATS schedule baseline (August 2026 – July 2028).

6.3. Critical path (dependency-based planning estimate)

The SEATS report does not publish a task-level critical path. Based on the planned release gates and logical dependencies, the provisional critical chain is:
I1 → I2 → E1 → E2 → C1 → C2 → T1 → C3 → T2 → P1 → Close-out. The C4 → T3 (Release 2.1) branch runs in parallel with P1 and carries planning float before close-out, so it does not drive the finish date. P1 pilot measurement runs in parallel with C4 and T3, but its longer duration controls the planned finish; close-out depends on both P1 and T3. Total path duration is 516 working days ≈ 24 calendar months. Any slippage on the critical chain directly extends the project finish date. The CPM values below are provisional planning estimates and should be validated against the resource-loaded calendar before baselining.

ID	Activity / Milestone	Dur (wd)	Predecessor(s)	ES	EF	LS	LF	TS	Critical	Early start
I1	Inception — initial elicitation	16	Start	0	16	0	16	0	Yes	03 Aug 2026
I2	Vision, plans and WBS / LCO	7	I1	16	23	16	23	0	Yes	25 Aug 2026
E1	Use cases and SRS requirements	10	I2	23	33	23	33	0	Yes	03 Sep 2026
E2	Architecture, analysis, prototype / LCA	27	E1	33	60	33	60	0	Yes	17 Sep 2026
C1a	Table map and hold workflow	40	E2	60	100	60	100	0	Yes	26 Oct 2026

ID	Activity / Milestone	Dur (wd)	Predecessor(s)	ES	EF	LS	LF	TS	Critical	Early start
C1b	Payment and staff access	40	E2	60	100	60	100	0	Yes	26 Oct 2026
C2	QR, check-in, live view, audit / IOC	40	C1a, C1b	100	140	100	140	0	Yes	21 Dec 2026
T1	Release 1.0 transition and go-live	25	C2	140	165	140	165	0	Yes	15 Feb 2027
C3	Release 2.0 growth construction	60	T1	165	225	165	225	0	Yes	22 Mar 2027
T2	Release 2.0 testing and deployment	25	C3	225	250	225	250	0	Yes	14 Jun 2027
P1	Pilot operation and KPI monitoring	261	T2	250	511	250	511	0	Yes	19 Jul 2027
C4	Release 2.1 productization build	120	T2	250	370	371	491	121	No	19 Jul 2027
T3	Release 2.1 testing and deployment	20	C4	370	390	491	511	121	No	03 Jan 2028
CL	Closure and expansion decision	5	P1, T3	511	516	511	516	0	Yes	18 Jul 2028

Table 6.3. CPM results — early/late start and finish, total slack (TS), and provisional criticality (working-day offsets). Activities with Total Slack = 0 are on the critical path.

6.4. Milestone control points

Milestone	Target date	Acceptance / decision
LCO	2 Sep 2026	Lifecycle objectives, scope direction and project viability reviewed.
LCA	23 Oct 2026	Architecture and SRS baseline approved; re-run financial analysis.
IOC	26 Feb 2027	Core build ready for transition and pilot readiness checks.
Release 1.0 live	2 Apr 2027	Core reservation and QR check-in operating at La Loy.
Release 2.0 live	30 Jul 2027	Growth features available; pilot year begins.
Release 2.1	11 Feb 2028	Productized multi-tenant version ready.
Expansion decision / closure	28 Jul 2028	Review pilot KPIs, waiting-list threshold, operating costs, hand-over and sponsor/customer sign-off.

7. Conclusion

The SEATS project is planned from 3 August 2026 to 28 July 2028, with three product releases and a pilot year. The source budget is 1,010,590 THB, including reserves, with 846,600 THB in labor cost for 2,632 hours. The WBS task split and the critical-path chain in this document are provisional planning estimates prepared to complete the requested project-management deliverables; they should be reviewed by the team and baselined at the Lifecycle Architecture milestone. The scope baseline (Sections 1–2), the effort and resource baselines (Sections 3–4), the cost baseline (Section 5) and the schedule baseline with the Gantt chart and critical path (Section 6) together form the Milestone 2 management baseline for the system, consistent with the SEATS Milestone 1 Part 2 Final Deliverables.
